




PANDEMIC

Projeto de Gerência e Manutenção de software
Parte 2

Equipe



Geiziane Silva Gonçalves
Ítalo Ferreira da Silva,
Oliver Pereira de Almeida,
Patricia Carvalho de Moraes
Rafael Roza de Abreu Soares e
Fernando René Cabral Araújo Filho




 <https://github.com/Rarkunho/pandemic-uff-gpms-ps.git>  





CONTROLE DE VERSÕES

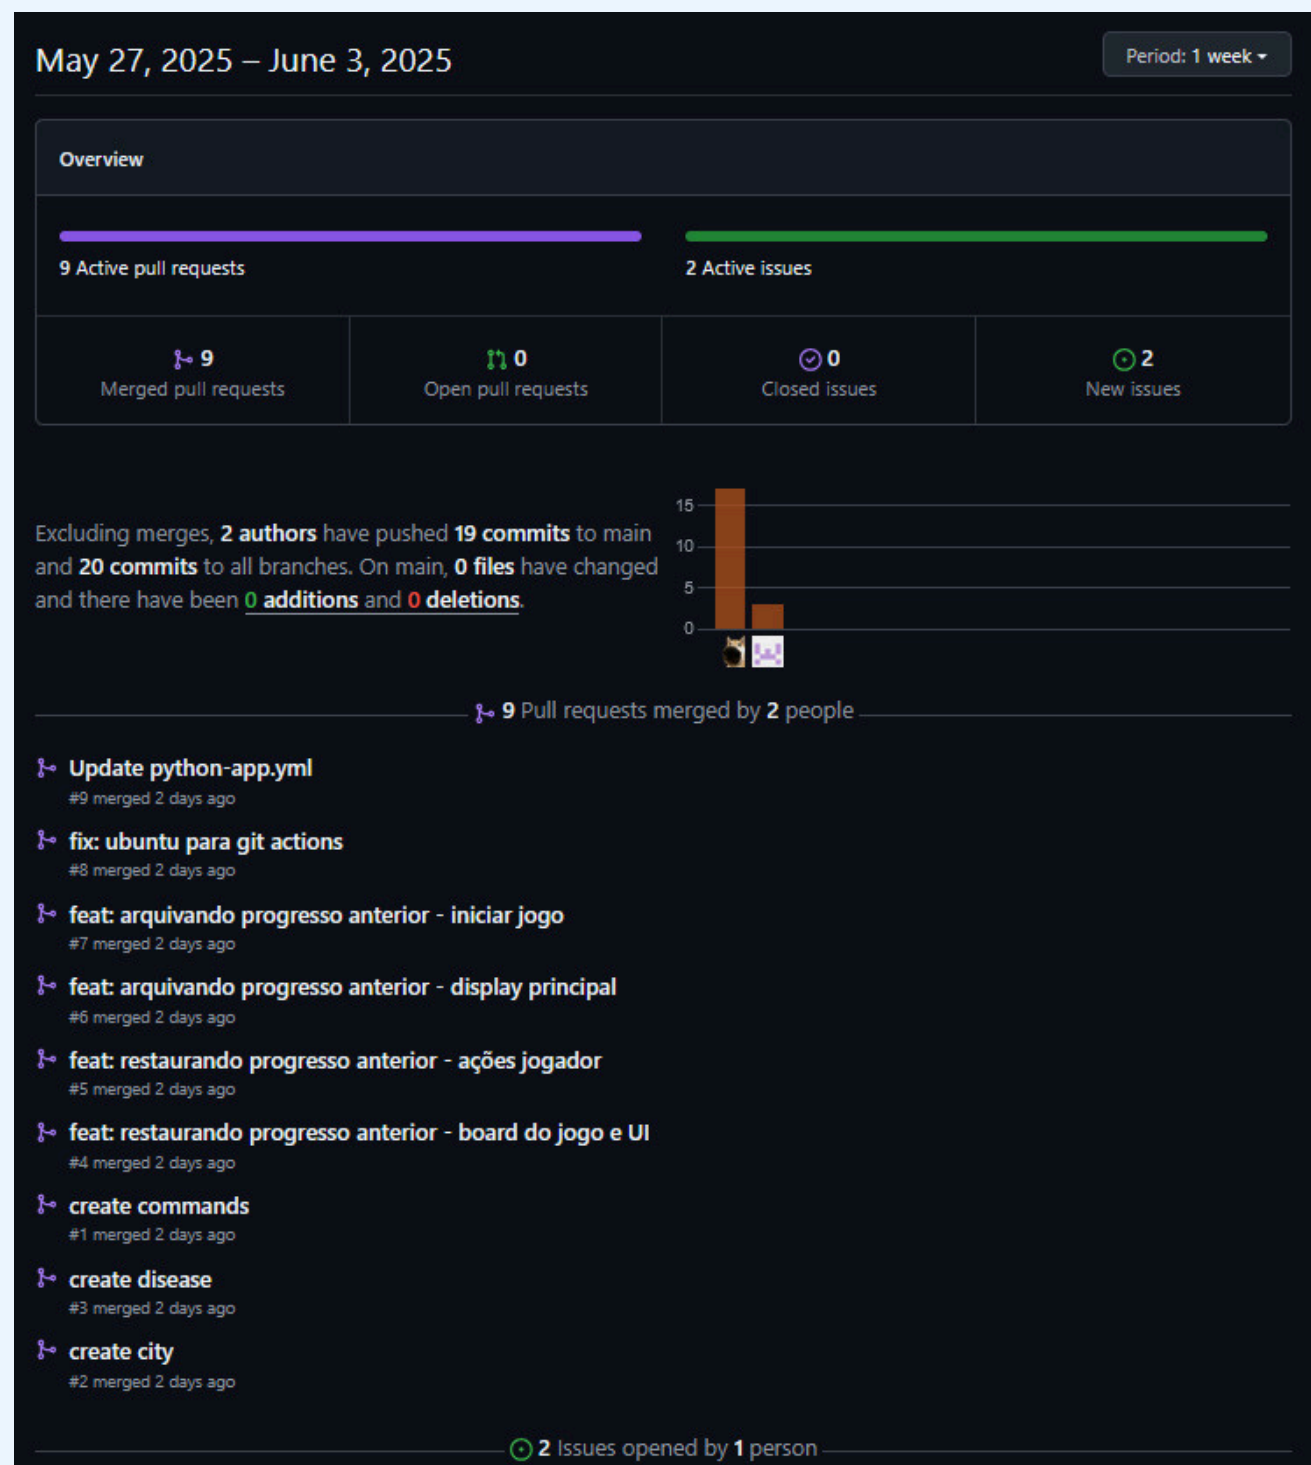

Update python-app.yml #9

Merged Rarkunho merged 5 commits into `main` from `git-action` 2 days ago

Conversation 0 Commits 5 Checks 2 Files changed 1

Rarkunho commented 2 days ago Owner

No description provided.

Rarkunho added 5 commits 2 days ago


- Update python-app.yml Verified ✗ d2990c1
- fix: py ao invés de py3 ✗ 281bac0
- fix: timeout ✗ 3856c08
- fix: continue on error ✗ 91d6ac5
- fix: continue on error run ✓ 5d71206

Rarkunho merged commit `f0c60d4` into `main` 2 days ago 2 checks passed View details Revert

Pull request successfully merged and closed Delete branch

You're all set — the `git-action` branch can be safely deleted.


CONTROLE DE MODIFICAÇÕES

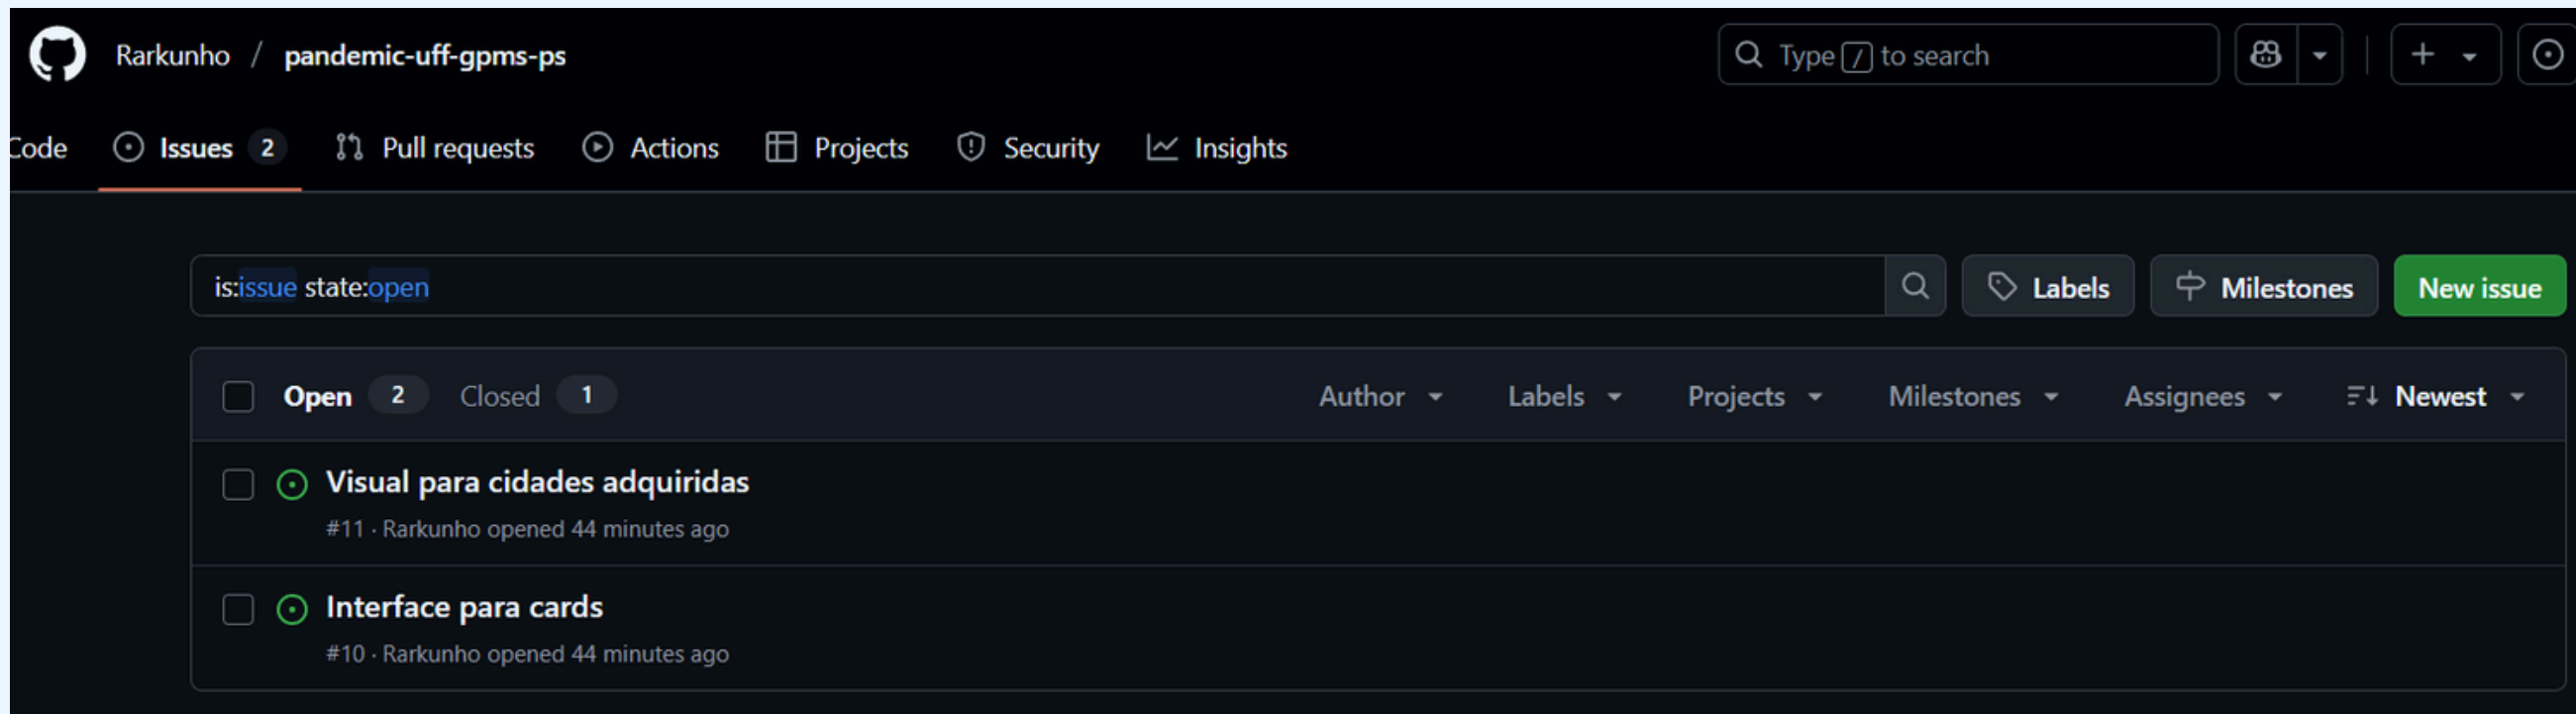

GitHub interface for repository **Rarkunho / pandemic-uff-gpms-ps**. The **Issues** tab is active, showing 2 open issues. The search bar contains `is:issue state:open`. The issue list shows:

- ☐ **Open 2** Closed 1
- ☐ **Visual para cidades adquiridas**
#11 · Rarkunho opened 44 minutes ago
- ☐ **Interface para cards**
#10 · Rarkunho opened 44 minutes ago

Navigation buttons: Labels, Milestones, New issue. Sorting: Newest.

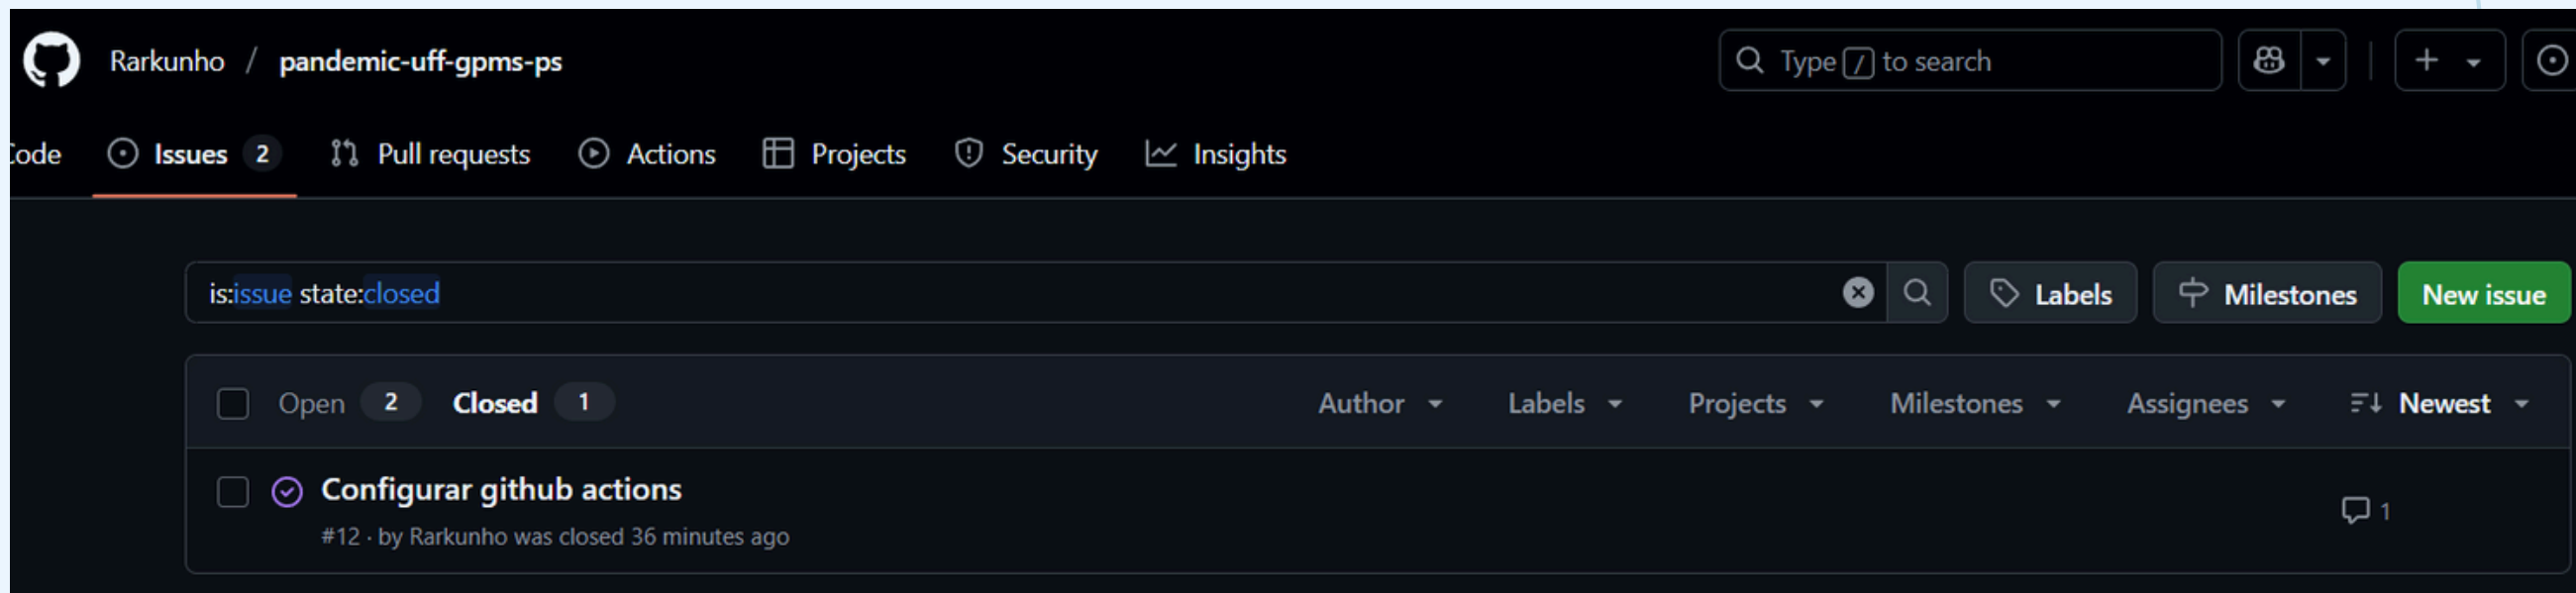

GitHub interface for repository **Rarkunho / pandemic-uff-gpms-ps**. The **Issues** tab is active, showing 2 closed issues. The search bar contains `is:issue state:closed`. The issue list shows:


- ☐ Open 2 **Closed 1**
- ☐ **Configurar github actions**
#12 · by Rarkunho was closed 36 minutes ago

Navigation buttons: Labels, Milestones, New issue. Sorting: Newest.



4


CONTROLE DE MODIFICAÇÕES

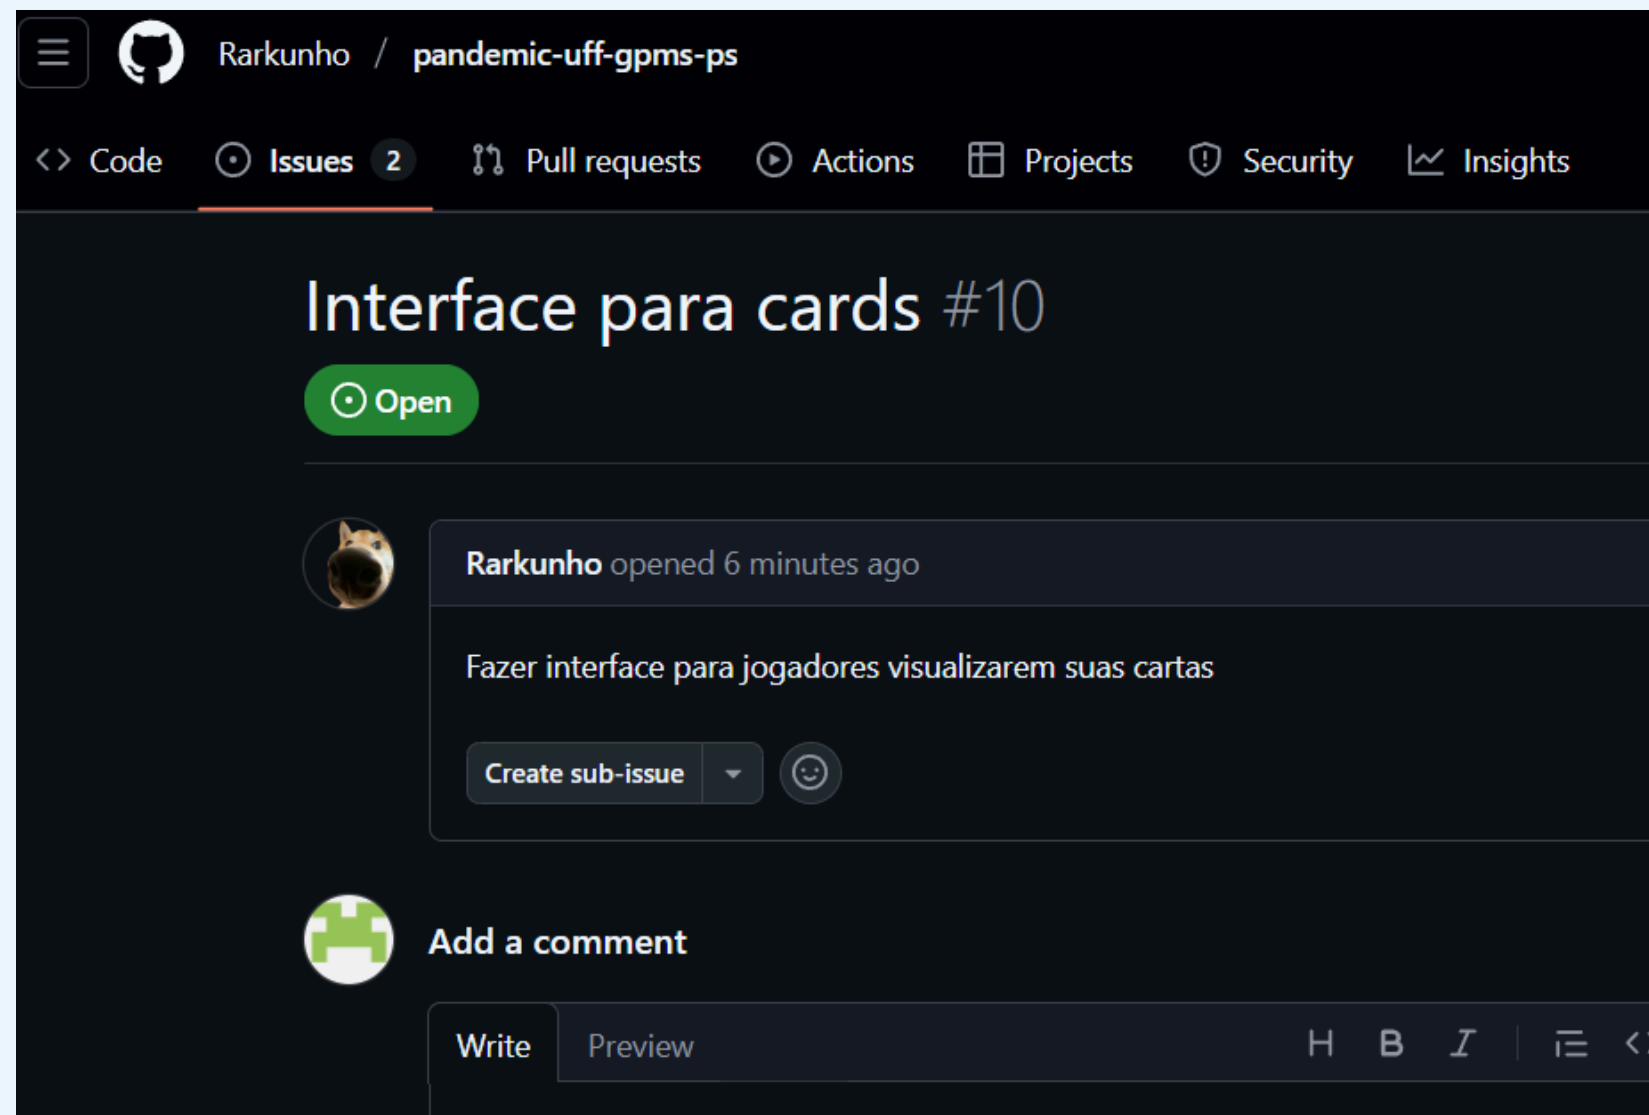



ESTRATÉGIA DE RAMIFICAÇÃO


Para esse repositório, foi utilizada a estratégia de Subsistemas

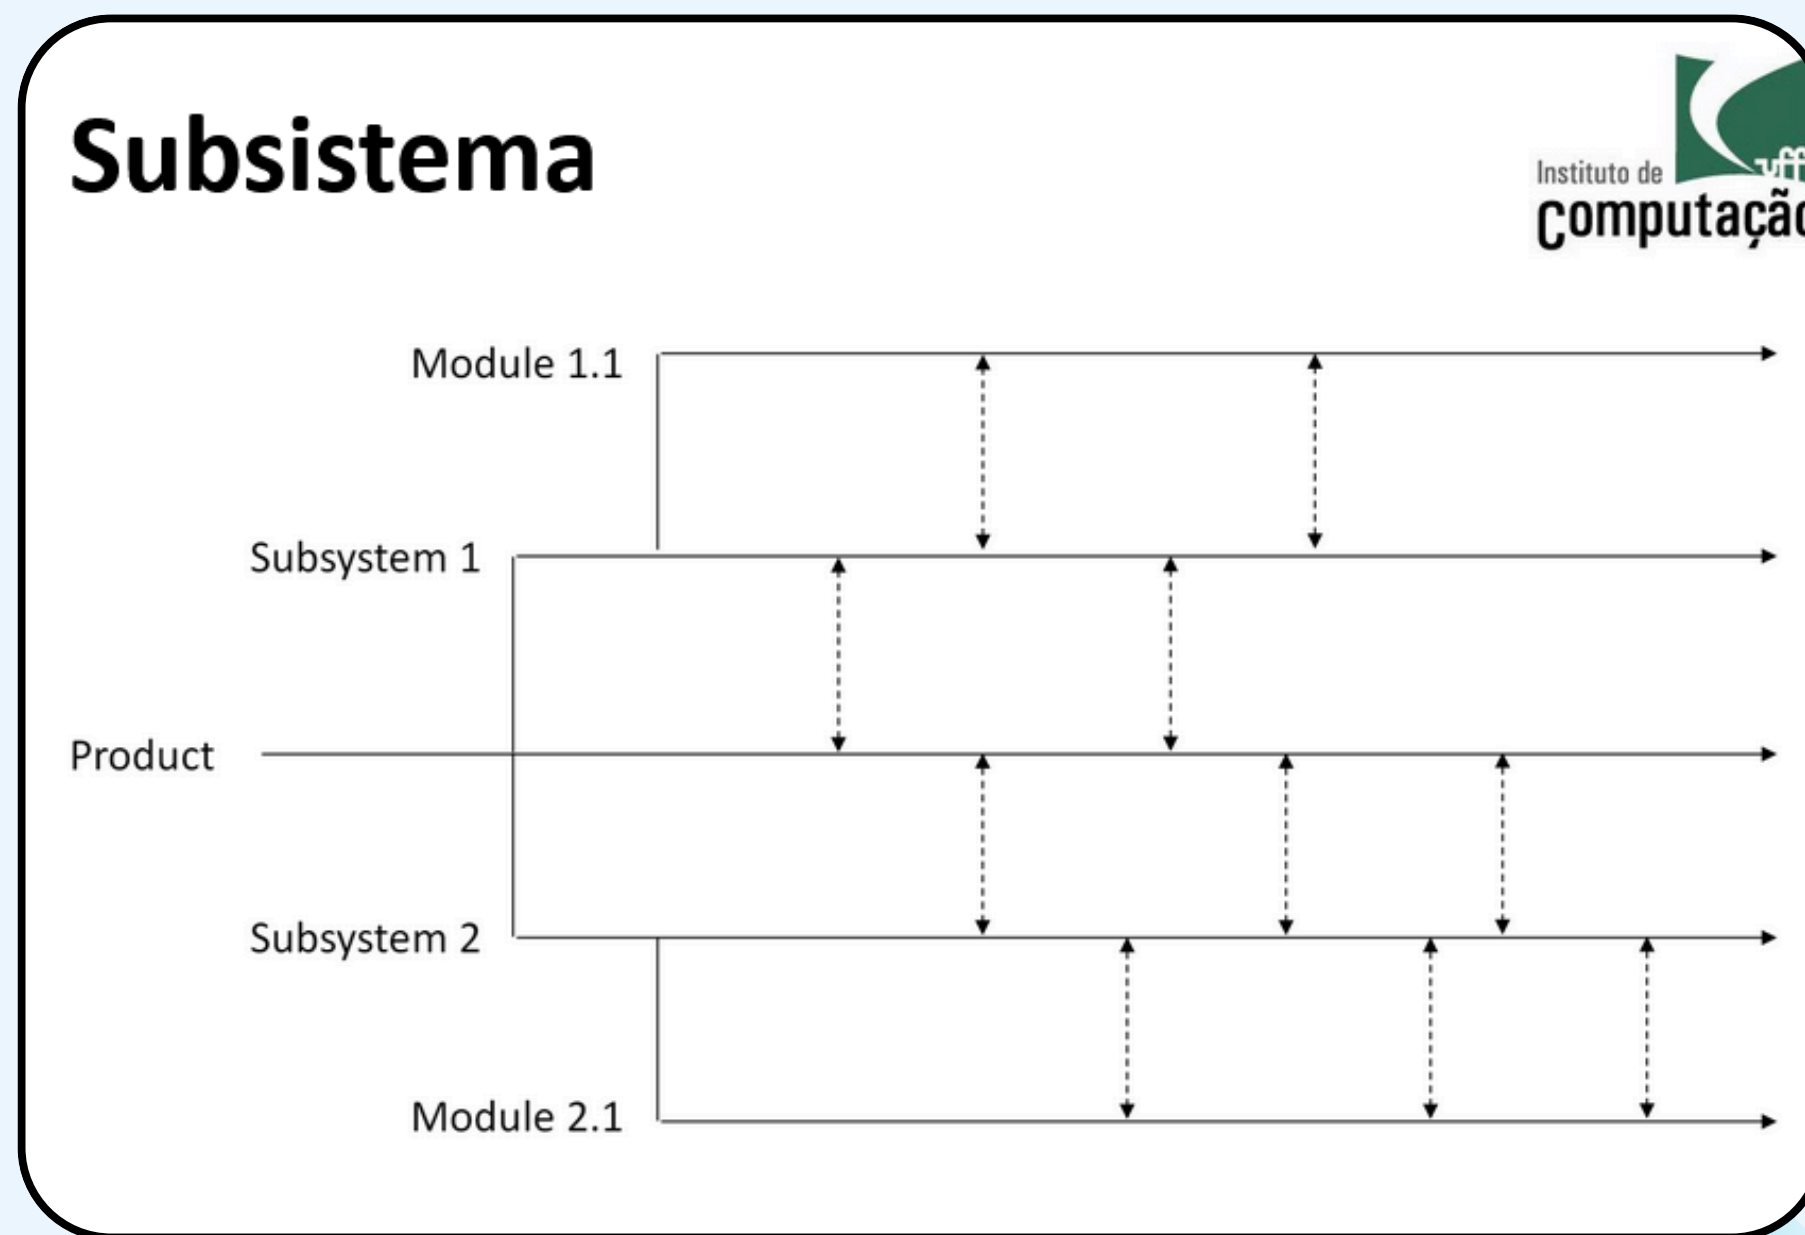



ESTRATÉGIA DE RAMIFICAÇÃO

O jogo se utiliza de vários arquivos diferentes para cada sistema e aspecto principal do jogo. Fazer uma branch para cada arquivo facilitou o desenvolvimento pois cada arquivo pode ser desenvolvido utilizando a main como base

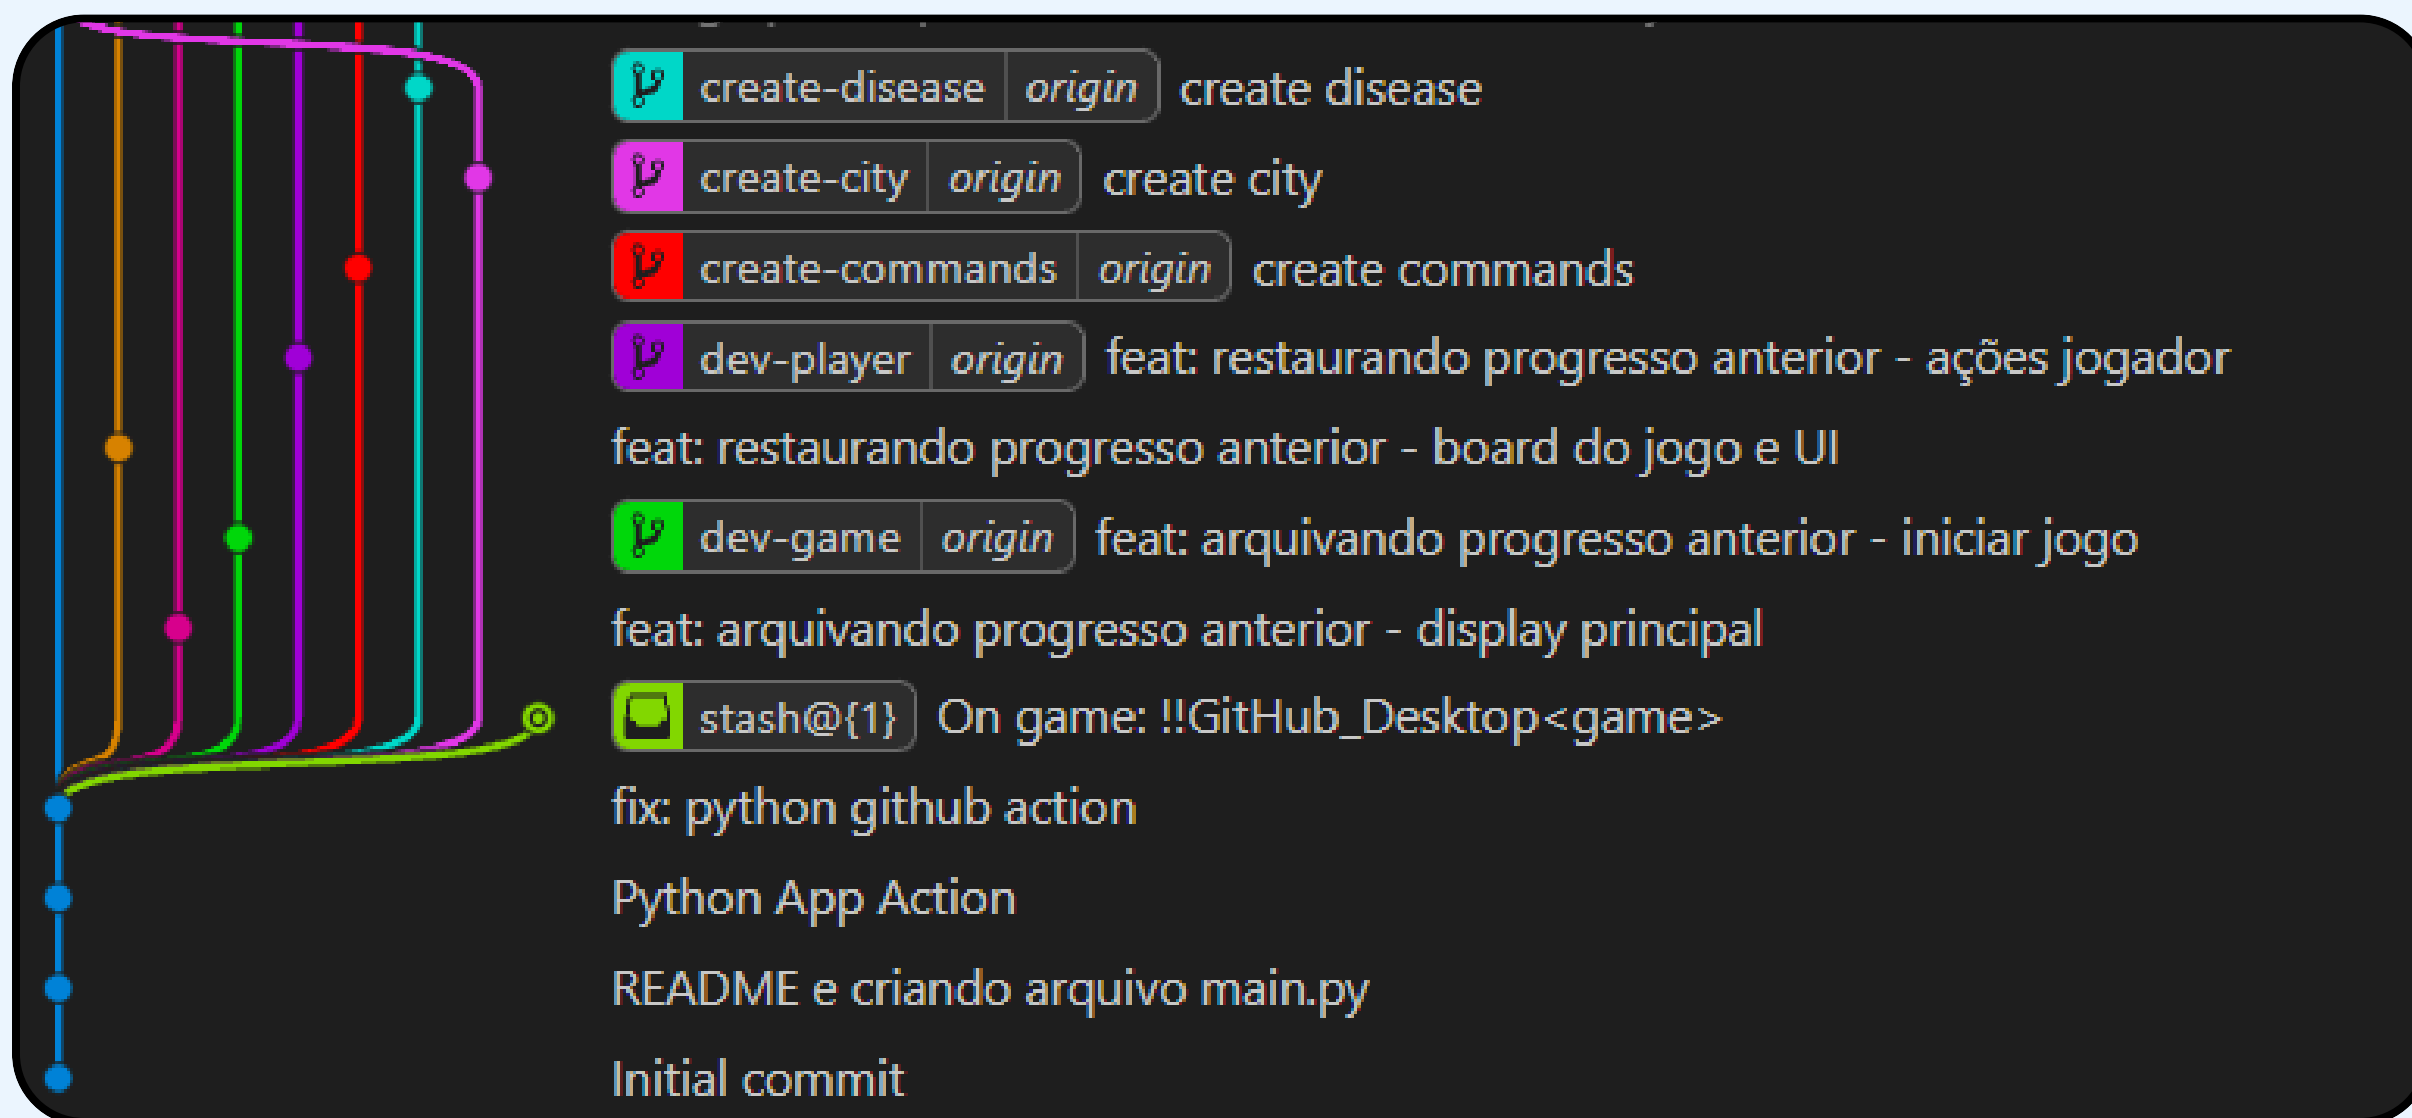



dev-main Merge branch 'main' into dev-main

main

create-city

create-commands

create-disease

dev-board

dev-game

dev-player

Merge pull reques... 2 Jun 2025 22:57 Italo b3afa0f6
1 Jun 2025 21:40 Rarkunho f0c60d44



APROVAÇÕES E INTEGRAÇÃO CONTÍNUA

Criamos um github action para python application que faz uma verificação básica se o jogo está rodando. Ela é executada automaticamente nas branches e main para checar integridade do jogo.

All checks have passed

1 successful check

✓ Python application / build (push) Successful in 1m

Details

Workflow file for this run

.github/workflows/python-app.yml at f0c60d4

```
1 # This workflow will install Python dependencies, run tests and lint with a single version of Python
2 # For more information see: https://docs.github.com/en/actions/automating-builds-and-tests/building-and-testing-python
3
4 name: Python application
5
6 on: [ "push", "pull_request" ]
7
8 permissions:
9   contents: read
10
11 jobs:
12   build:
13
14     runs-on: windows-latest
15
16     steps:
17     - uses: actions/checkout@v4
18     - name: Set up Python 3.10
19       uses: actions/setup-python@v3
20       with:
21         python-version: "3.10"
22     - name: Install dependencies
23       run: |
24         python -m pip install --upgrade pip
25         pip install pygame
26     - name: Test main game
27       continue-on-error: true
28       run: |
29         python main.py
30       timeout-minutes: 1
31
```

build

succeeded 3 minutes ago in 1m 23s

Search logs

- > ✓ Set up job 1s
- > ✓ Run actions/checkout@v4 5s
- > ✓ Set up Python 3.10 0s
- > ✓ Install dependencies 14s
- > ✓ Test main game 1m 0s
- > ✓ Post Set up Python 3.10 0s
- > ✓ Post Run actions/checkout@v4 1s
- > ✓ Complete job 0s

48 workflow runs

Event Status Branch Actor

✓ Merge pull request #9 from Rarkunho/git-action

Python application #48: Commit f0c60d4 pushed by Rarkunho

dev-player

6 minutes ago
1m 30s

...

✓ Merge pull request #9 from Rarkunho/git-action

Python application #47: Commit f0c60d4 pushed by Rarkunho

create-commands

6 minutes ago
1m 27s

...

✓ Merge pull request #9 from Rarkunho/git-action

Python application #46: Commit f0c60d4 pushed by Rarkunho

create-city

6 minutes ago
1m 51s

...

✓ Merge pull request #9 from Rarkunho/git-action

Python application #45: Commit f0c60d4 pushed by Rarkunho

dev-game

7 minutes ago
1m 47s

...

✓ Merge pull request #9 from Rarkunho/git-action

Python application #44: Commit f0c60d4 pushed by Rarkunho

create-disease

7 minutes ago
1m 34s

...



MONITORAMENTO

Labels

Milestones

Edit

Close Milestone

New issue

3º entrega do trabalho

Open

Due by July 1, 2025 Last updated now

0% complete

"A terceira apresentação deve apresentar a versão final do produto (demo), as dificuldades e decisões tomadas ao longo do desenvolvimento, o histórico de versões no controle de versões, além de todos os dados de monitoramento e controle do projeto (conforme descrito anteriormente). Se o grupo não tiver apresentado Pull Requests e integração contínua na segunda apresentação, pode-se apresentar nesta apresentação para o bônus. Caso o grupo deseje que o professor pondere a nota por membro do grupo, deve ser informada nesta apresentação a participação de cada membro do grupo no trabalho (PV e EV de cada membro)."

Show less ^



Open

0

Closed

0

There are no open issues in this milestone

Add issues to milestones to help organize your work for a particular release or project. Find and add [issues with no milestones](#) in this repo.






GANNT

		Nome	Duração	Início	Fim	Nomes dos Recursos	Sucessores
1		Pandemic	63 dias?	04/04/2025 08:00	01/07/2025 17:00		
2		Produto	41,125 dias?	02/05/2025 08:00	30/06/2025 09:00		
3		Análise e Design	11 dias	02/05/2025 08:00	16/05/2025 17:00	Fernando;Italo	4
4		Mecânica de Jogo (Part...	7 dias?	19/05/2025 08:00	27/05/2025 17:00	Fernando;Italo	7;8;9;10;34
5		Interface (Parte 1)	2 dias?	06/05/2025 08:00	07/05/2025 17:00	Fernando;Italo;Oliver	
6		Testes (Parte 1)	4 dias?	12/05/2025 08:00	15/05/2025 17:00	Fernando;Italo;Oliver	
7		Controle de Jogadores (...)	14,25 dias?	16/05/2025 15:00	05/06/2025 17:00	Fernando;Italo	34;8;11
8		Sistemas de Ações de Jo...	11,5 dias?	27/05/2025 15:00	12/06/2025 10:00	Fernando;Italo	34;14
9		Sistemas e Doenças (Part...	8 dias?	26/05/2025 08:00	04/06/2025 17:00	Fernando;Italo	34;15
10		Mecânica de Jogo (Parte 2)	7 dias?	28/05/2025 08:00	05/06/2025 17:00		33;11;15
11		Controle de Jogadores (...)	5 dias?	06/06/2025 08:00	12/06/2025 17:00		33;14
12		Interface (Parte 2)	2 dias?	04/06/2025 08:00	05/06/2025 17:00		
13		Testes (Parte 2)	3 dias?	04/06/2025 08:00	06/06/2025 17:00		
14		Sistemas de Ações de Jo...	5,375 dias?	13/06/2025 08:00	20/06/2025 11:00		33
15		Sistemas e Doenças (Part...	7 dias?	19/06/2025 09:00	30/06/2025 09:00		33
16		Gerenciamento de projeto	3 dias?	02/05/2025 08:00	06/05/2025 17:00		
17		Estratégia de Ramificação	1 dia	02/05/2025 08:00	02/05/2025 17:00	Fernando;Italo;Oliver	4
18		Controle de Versões	1 dia	02/05/2025 08:00	05/05/2025 17:00	Todos	4
19		Cronograma (Gantt)	0,5 dias	05/05/2025 12:00	05/05/2025 17:00	Rafael	25
20		Custo e Orçamento	3 dias	02/05/2025 08:00	06/05/2025 17:00	Geiziane;Oliver	
21		Planning Poker	1 dia?	02/05/2025 08:00	05/05/2025 17:00	Todos	20
22		EAP	0,5 dias?	05/05/2025 08:00	05/05/2025 13:00	Geiziane;Rafael	19;35
23		Escopo	1 dia	02/05/2025 08:00	02/05/2025 17:00	Geiziane;Patricia;Rafael	22
24		Monitoramento e controle	61,667 dias?	04/04/2025 08:00	30/06/2025 14:20		
25		EVA (Parte 1)	3 dias?	05/05/2025 08:00	07/05/2025 17:00	Rafael;Geiziane;Patricia	26;27;35
26		Burndown (Parte 1)	3 dias?	06/05/2025 08:00	08/05/2025 17:00	Rafael;Geiziane	35;28
27		EVA (Parte 2)	2 dias?	02/06/2025 08:00	03/06/2025 17:00	Geiziane;Rafael	34;29
28		Burndown (Parte 2)	2 dias?	02/06/2025 08:00	03/06/2025 17:00	Patricia;Rafael	34;30
29		EVA (Parte 3)	0,667 dias	28/06/2025 08:00	30/06/2025 14:20	Geiziane;Patricia;Rafael	33
30		Burndown (Parte 3)	0,667 dias	28/06/2025 08:00	30/06/2025 14:20	Patricia;Geiziane;Rafael	33
31		Riscos	2 dias	04/04/2025 08:00	07/04/2025 17:00	Geiziane;Italo;Patricia;Rafael	35
32		Apresentações e Demos	41 dias	06/05/2025 08:00	01/07/2025 17:00		
33		Apresentação Final	0 dias	01/07/2025 20:00	01/07/2025 17:00		
34		Apresentação Intermedia...	0 dias	04/06/2025 08:00	12/06/2025 10:00	Todos	
35		Apresentação Inicial	0,748 dias	06/05/2025 08:00	07/05/2025 08:59	Todos	





GANNT GRÁFICO

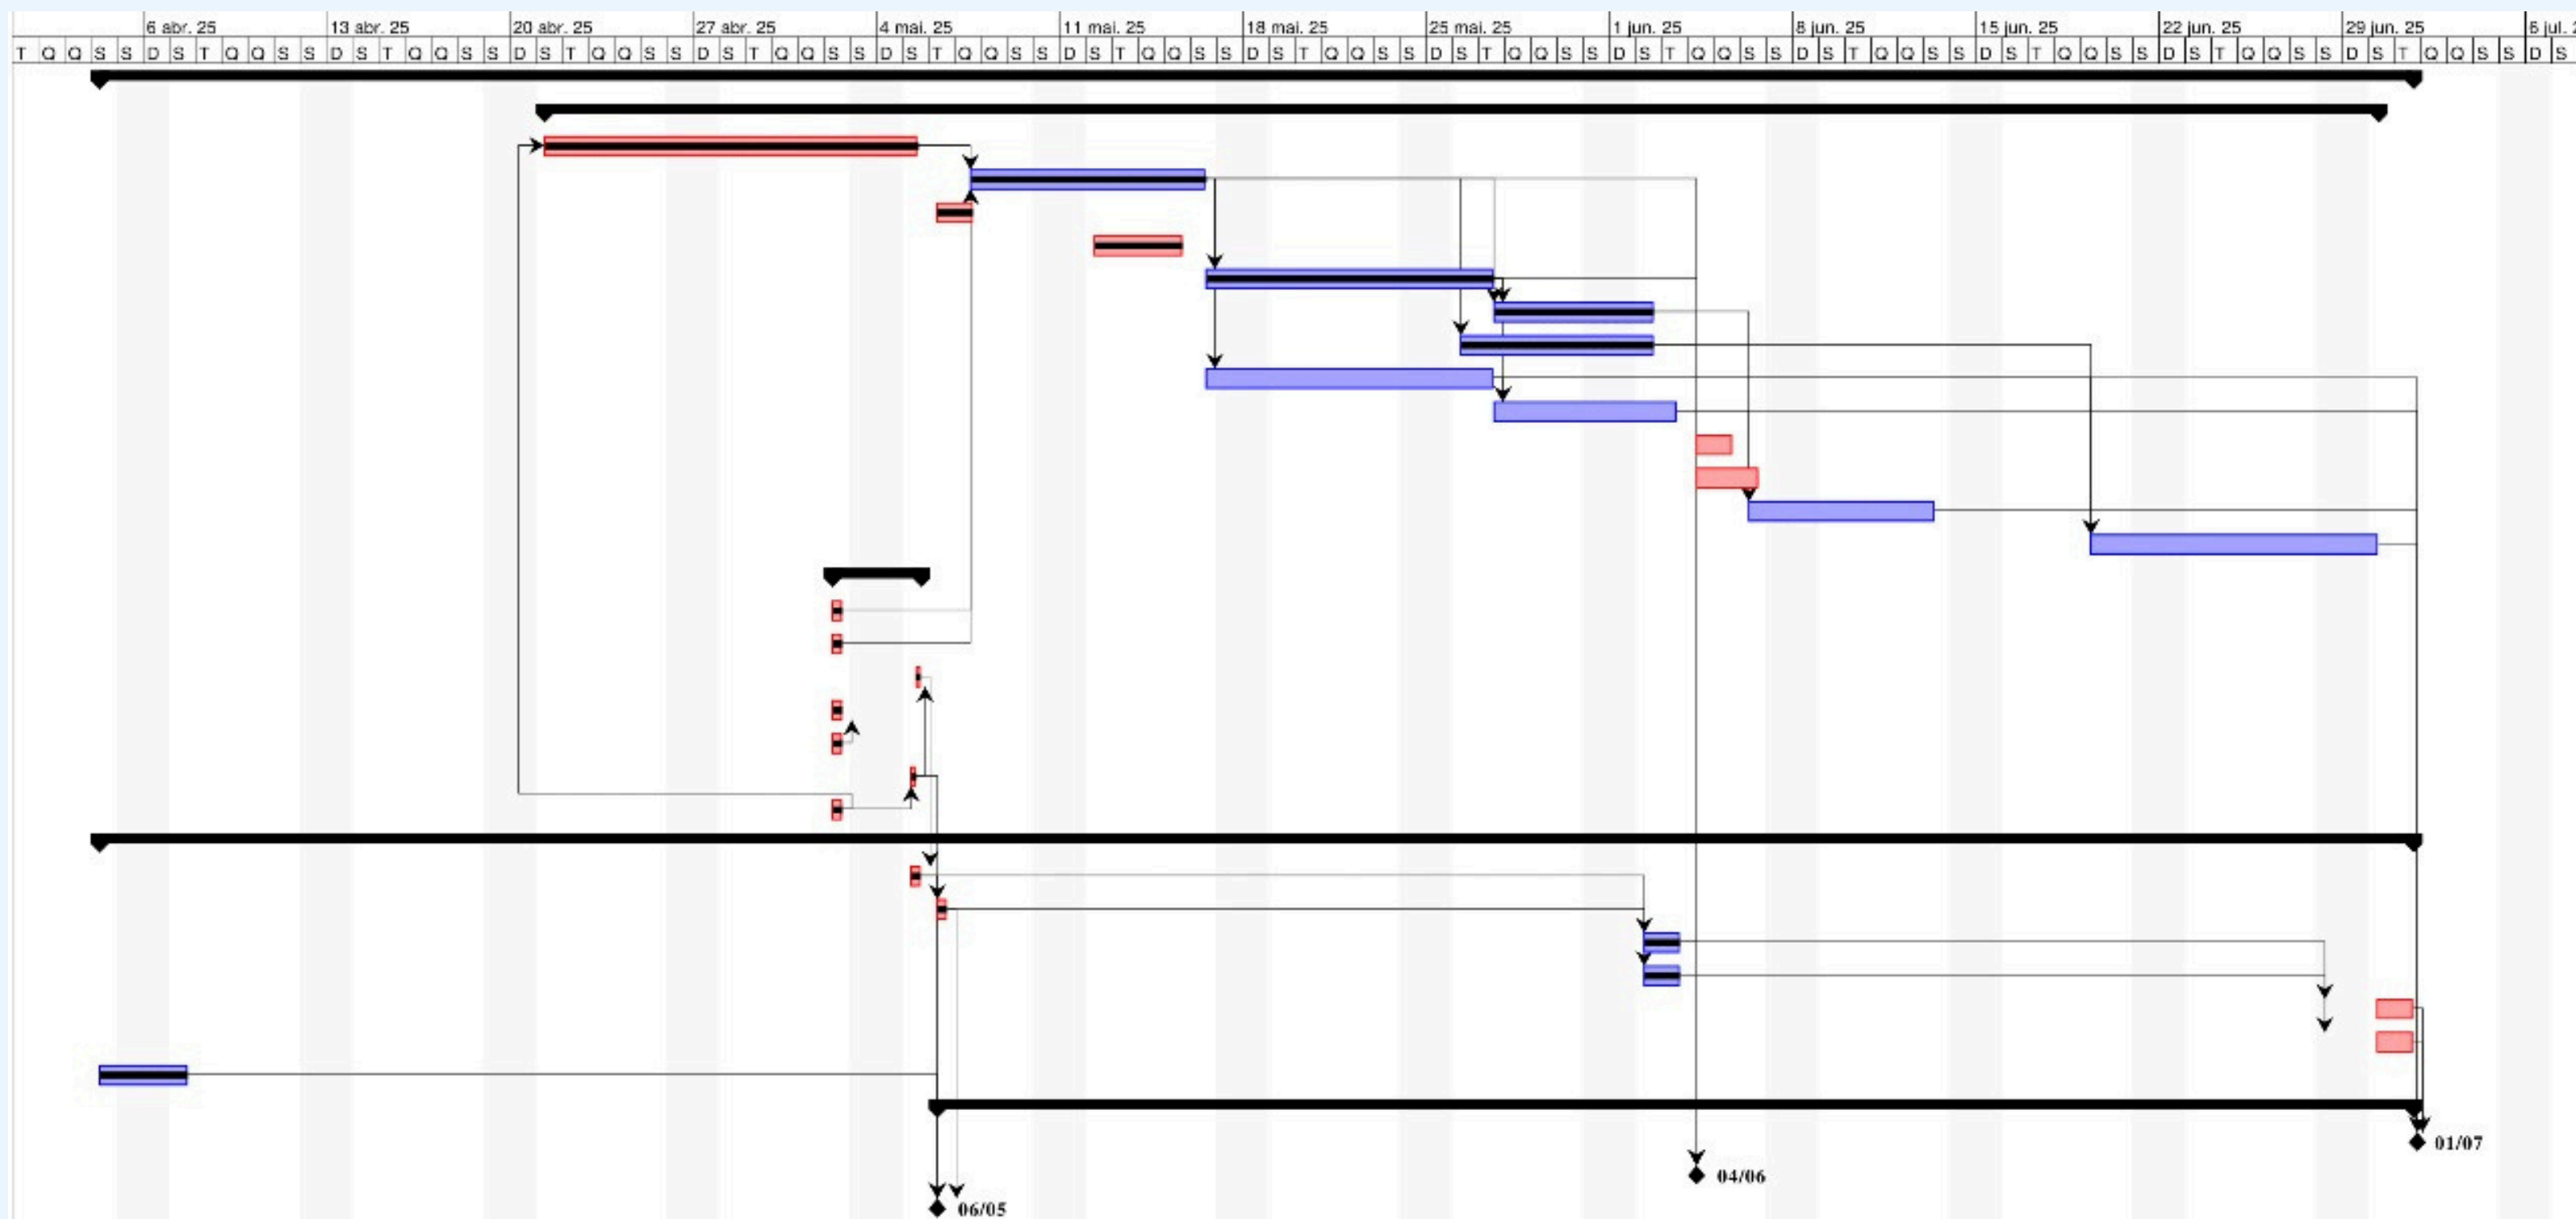




EVA

Marcos	SPI	CPI	%conclusão(r eal)
05/05/2025	1,18	1,249665247	0,3806451613
03/06/2025	0,9957081545	1,19467298	0,7483870968


Analise de Valor Agregado (EVA)

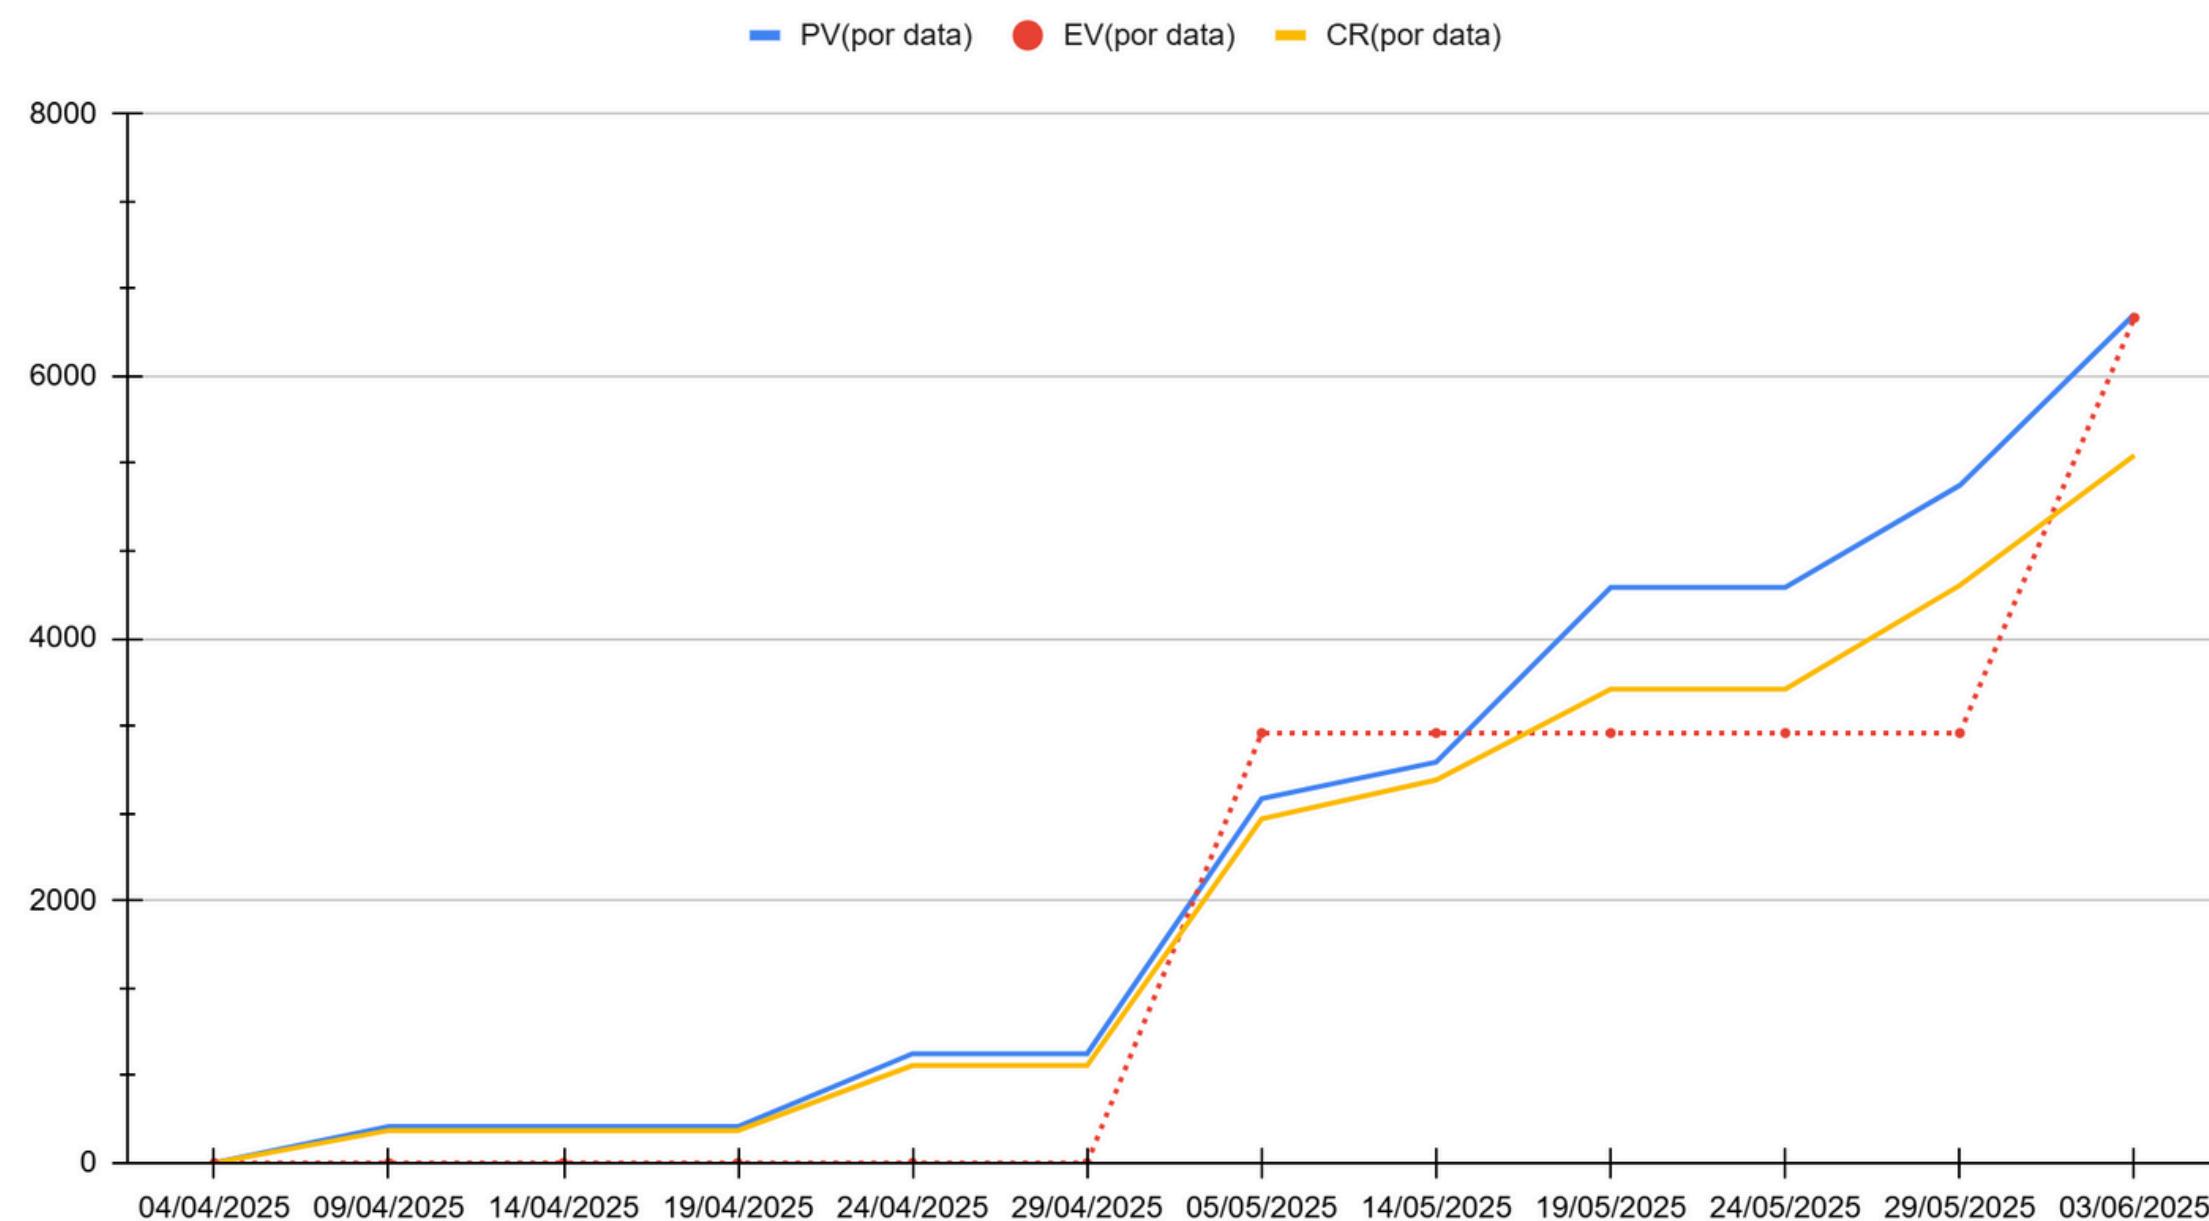




BURNDOWN

Burndown (parte 2)


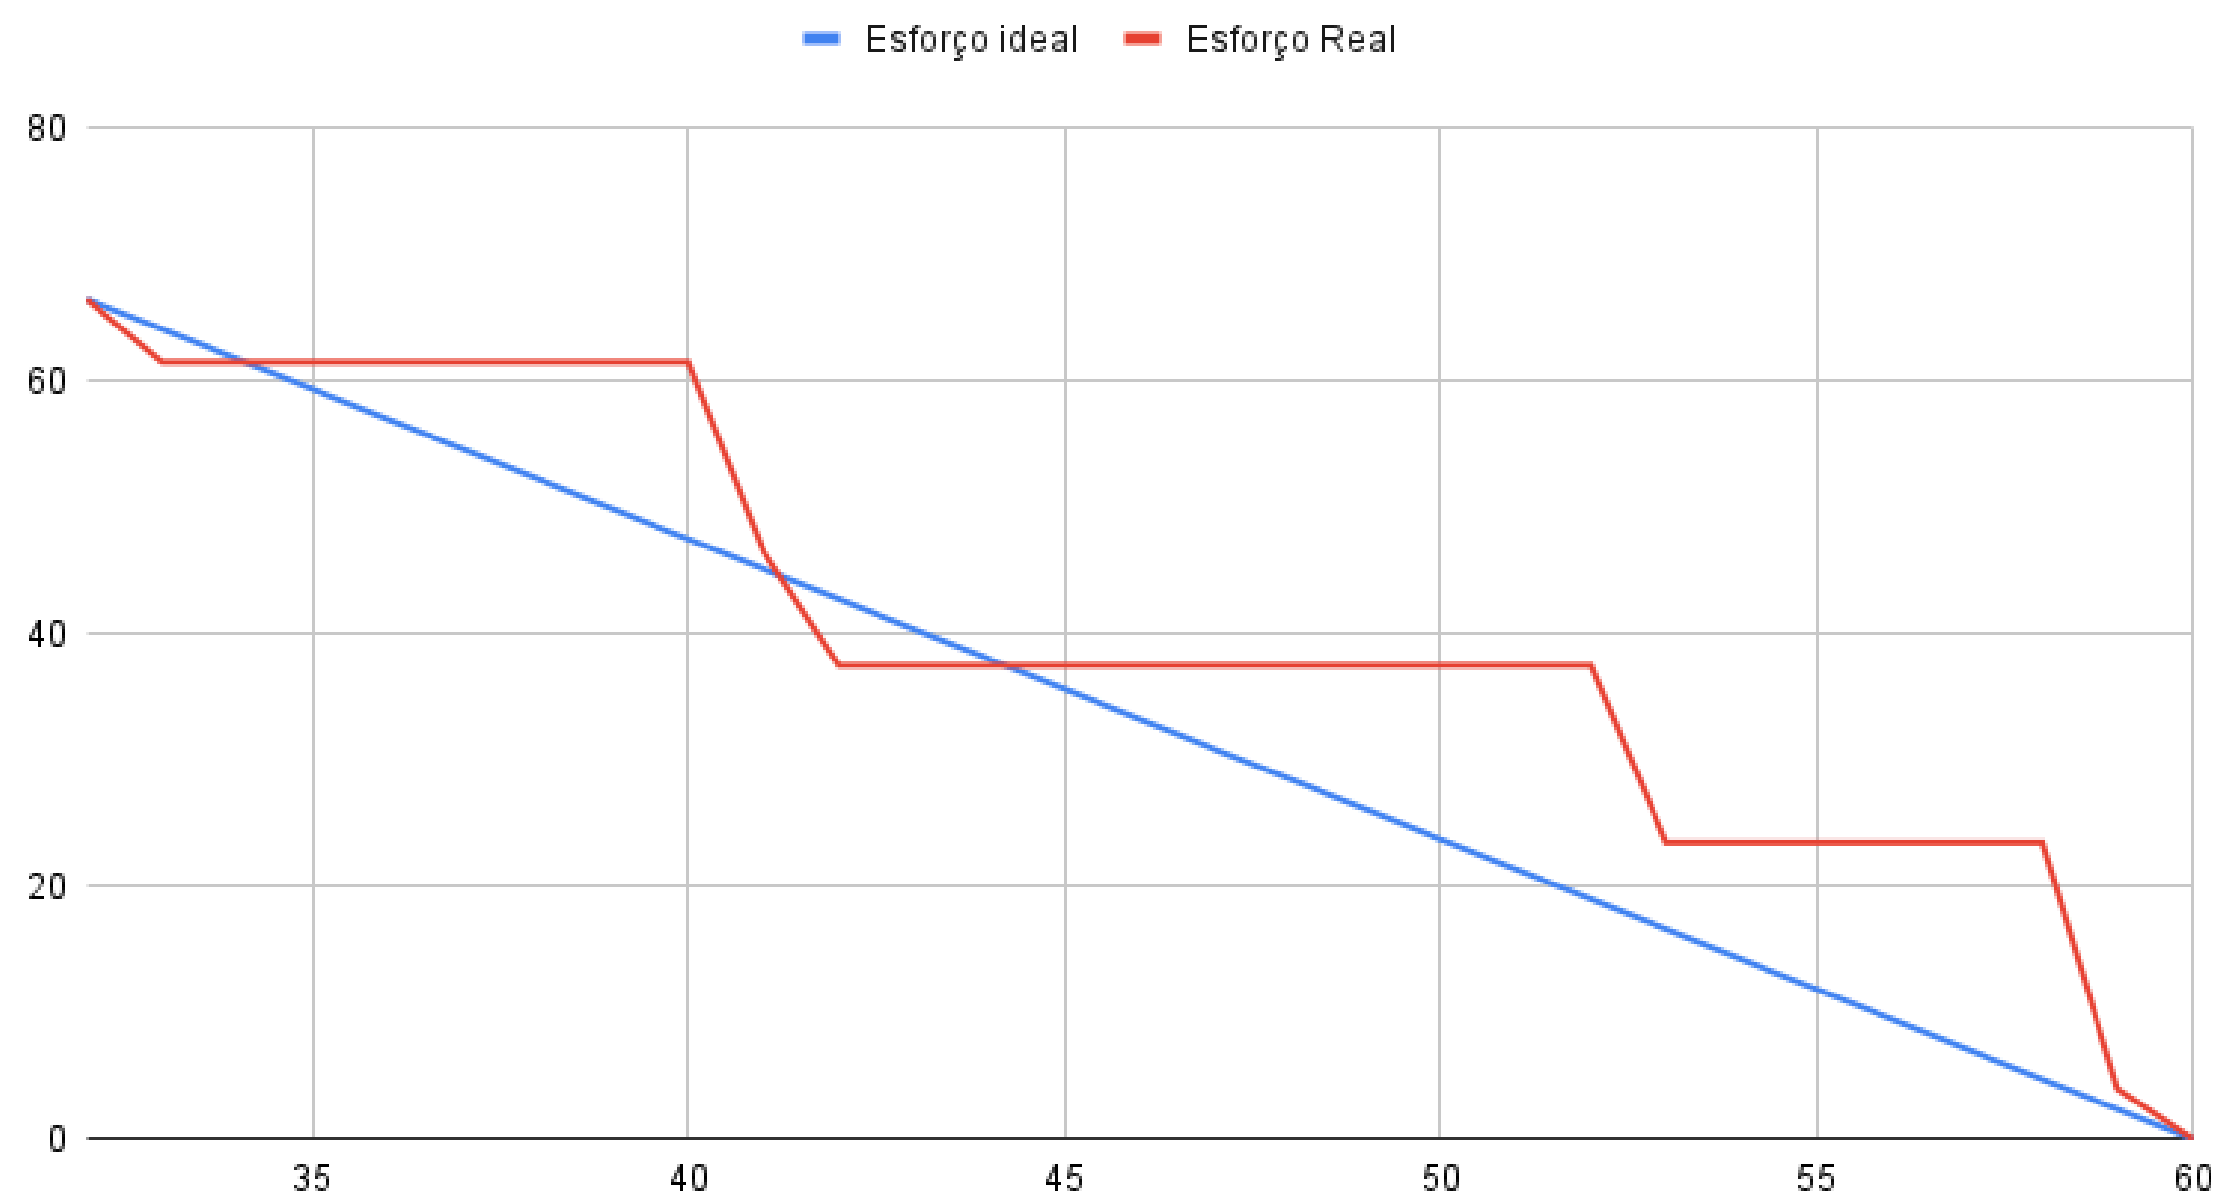






Demo

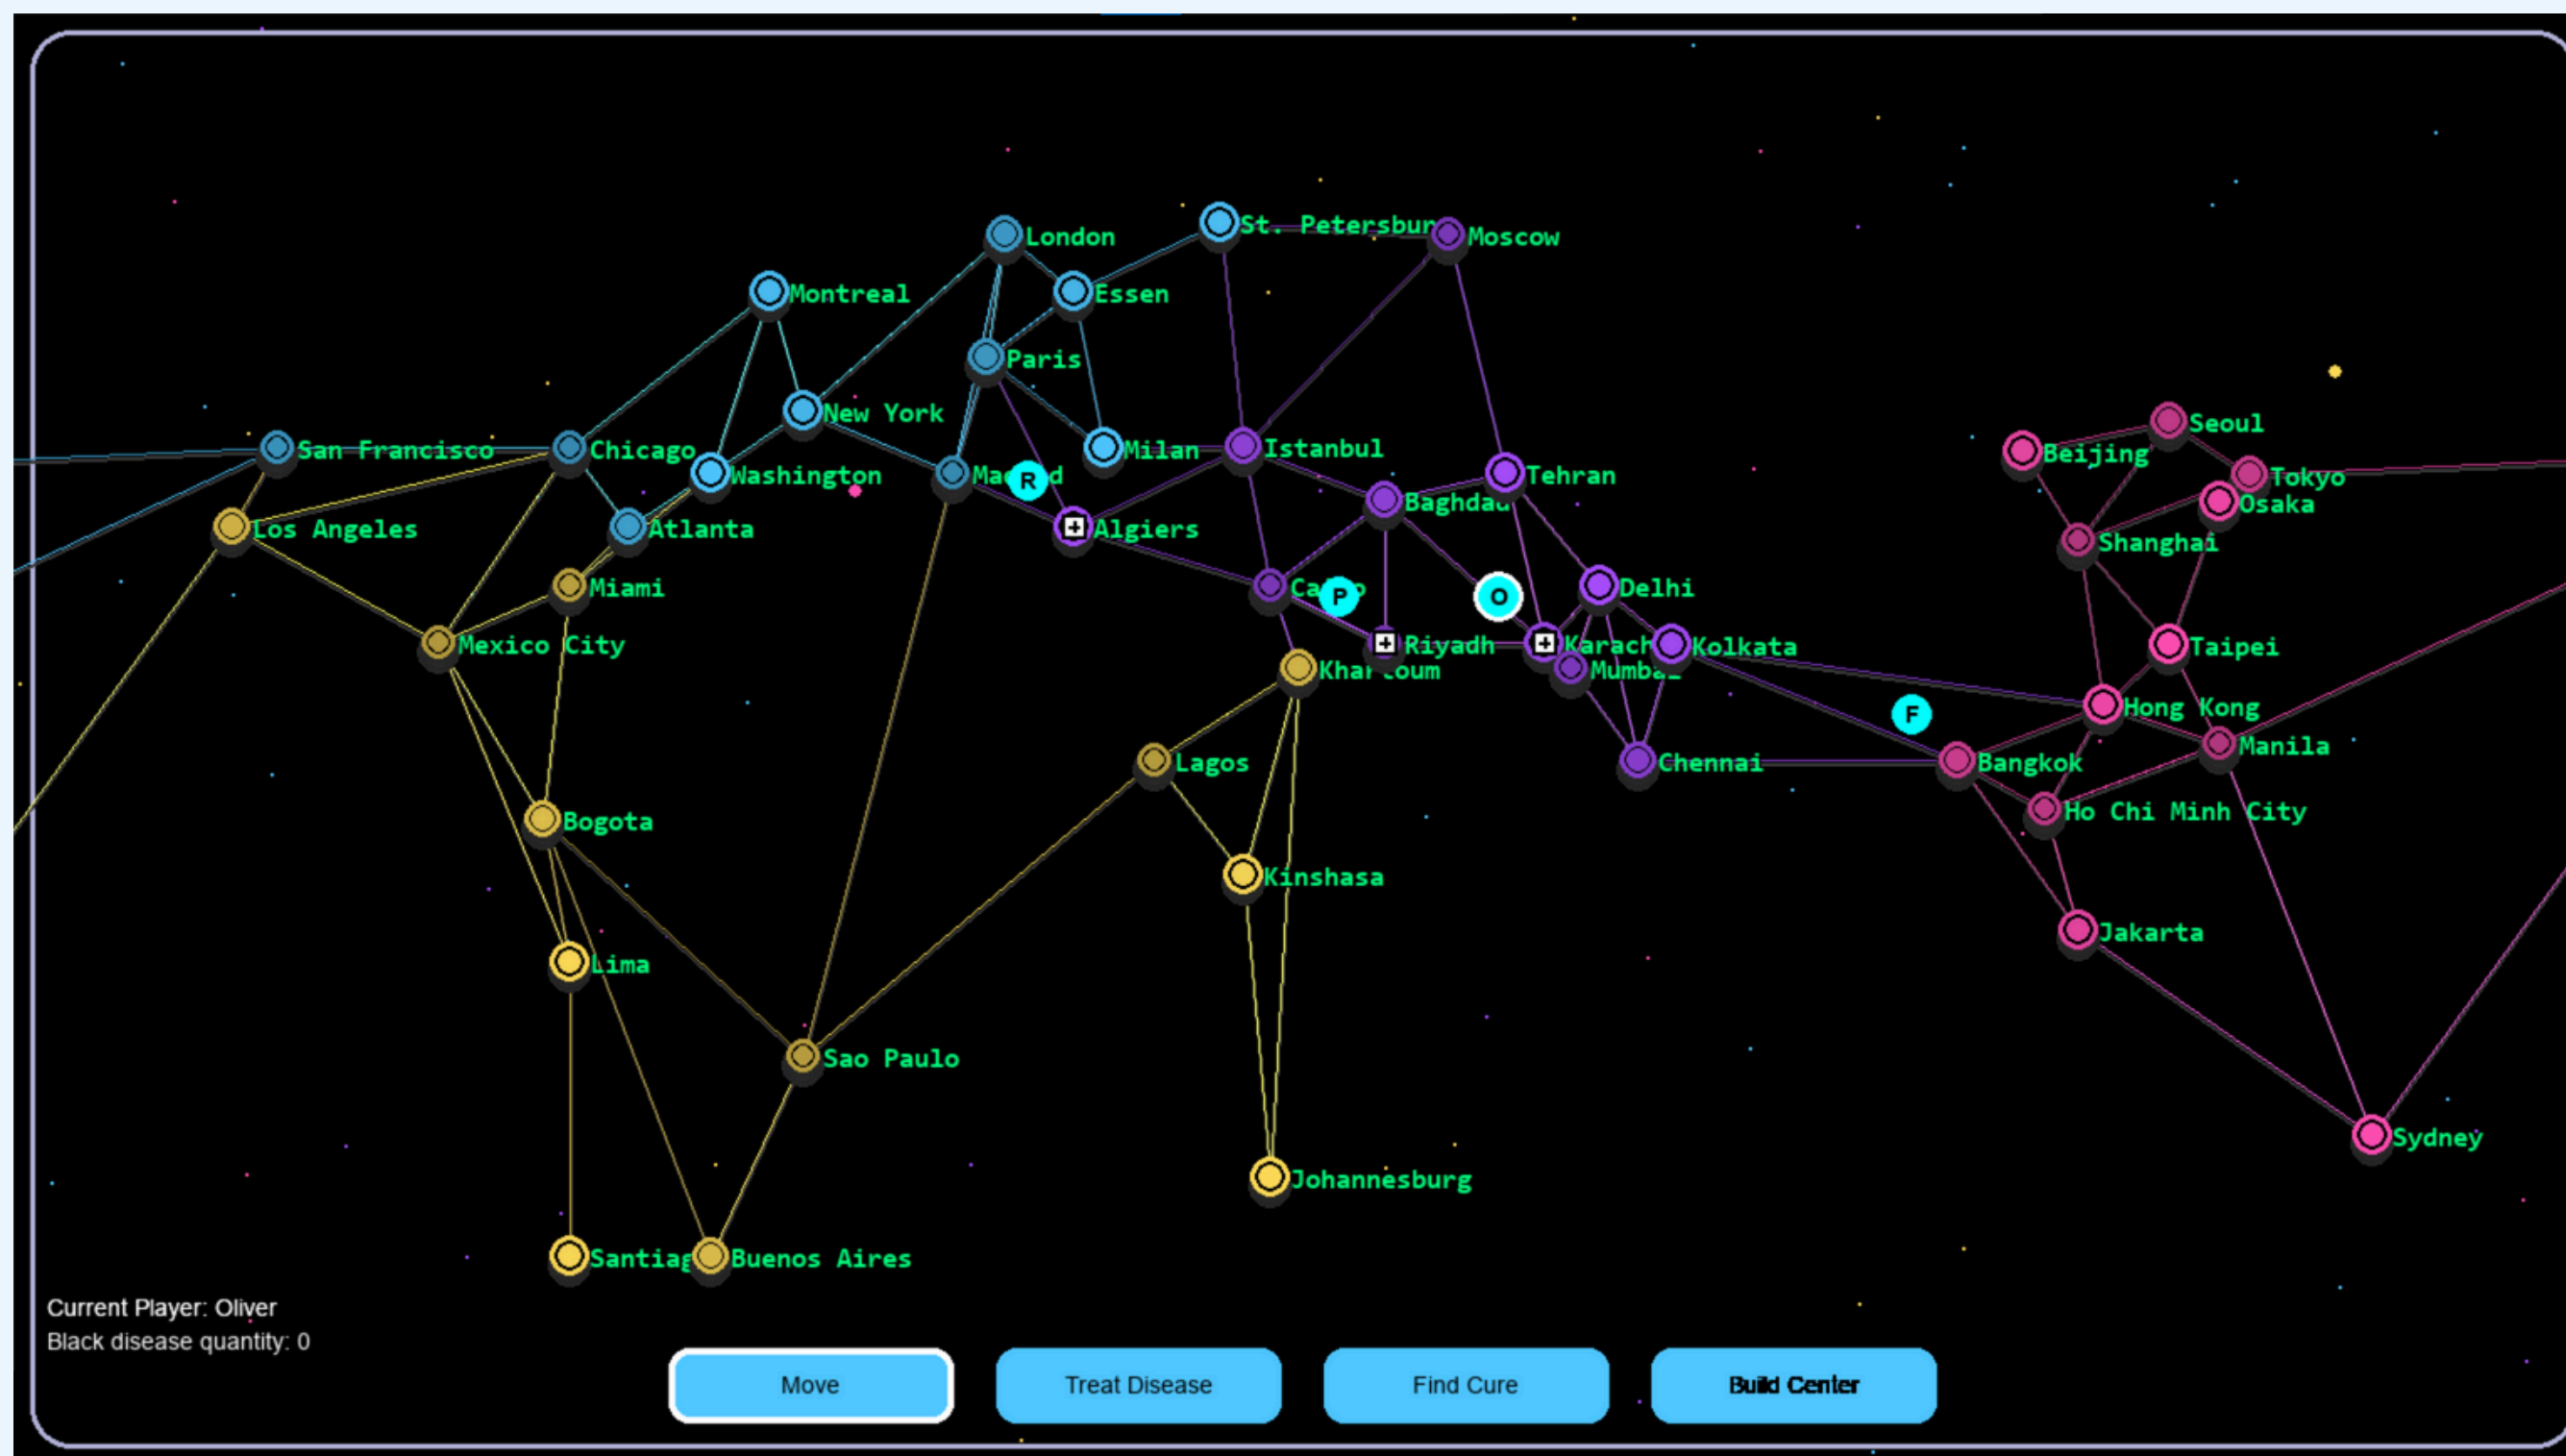



Demo - Movimentação

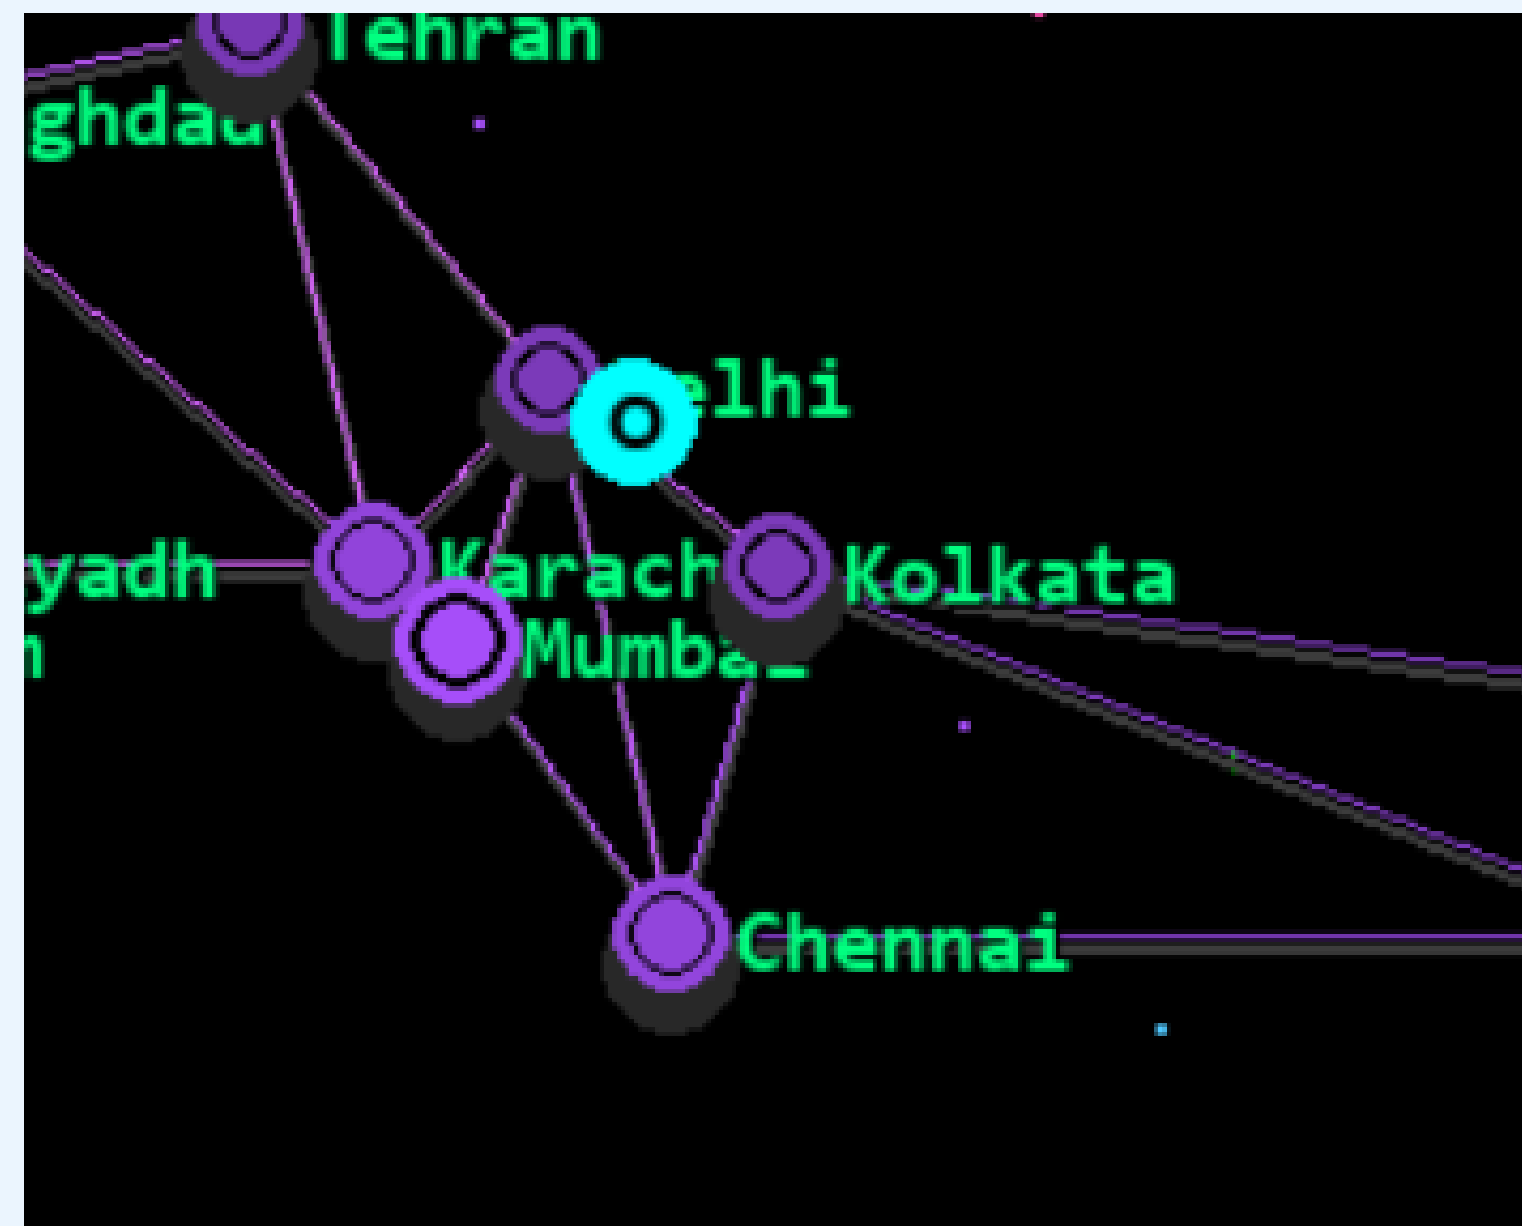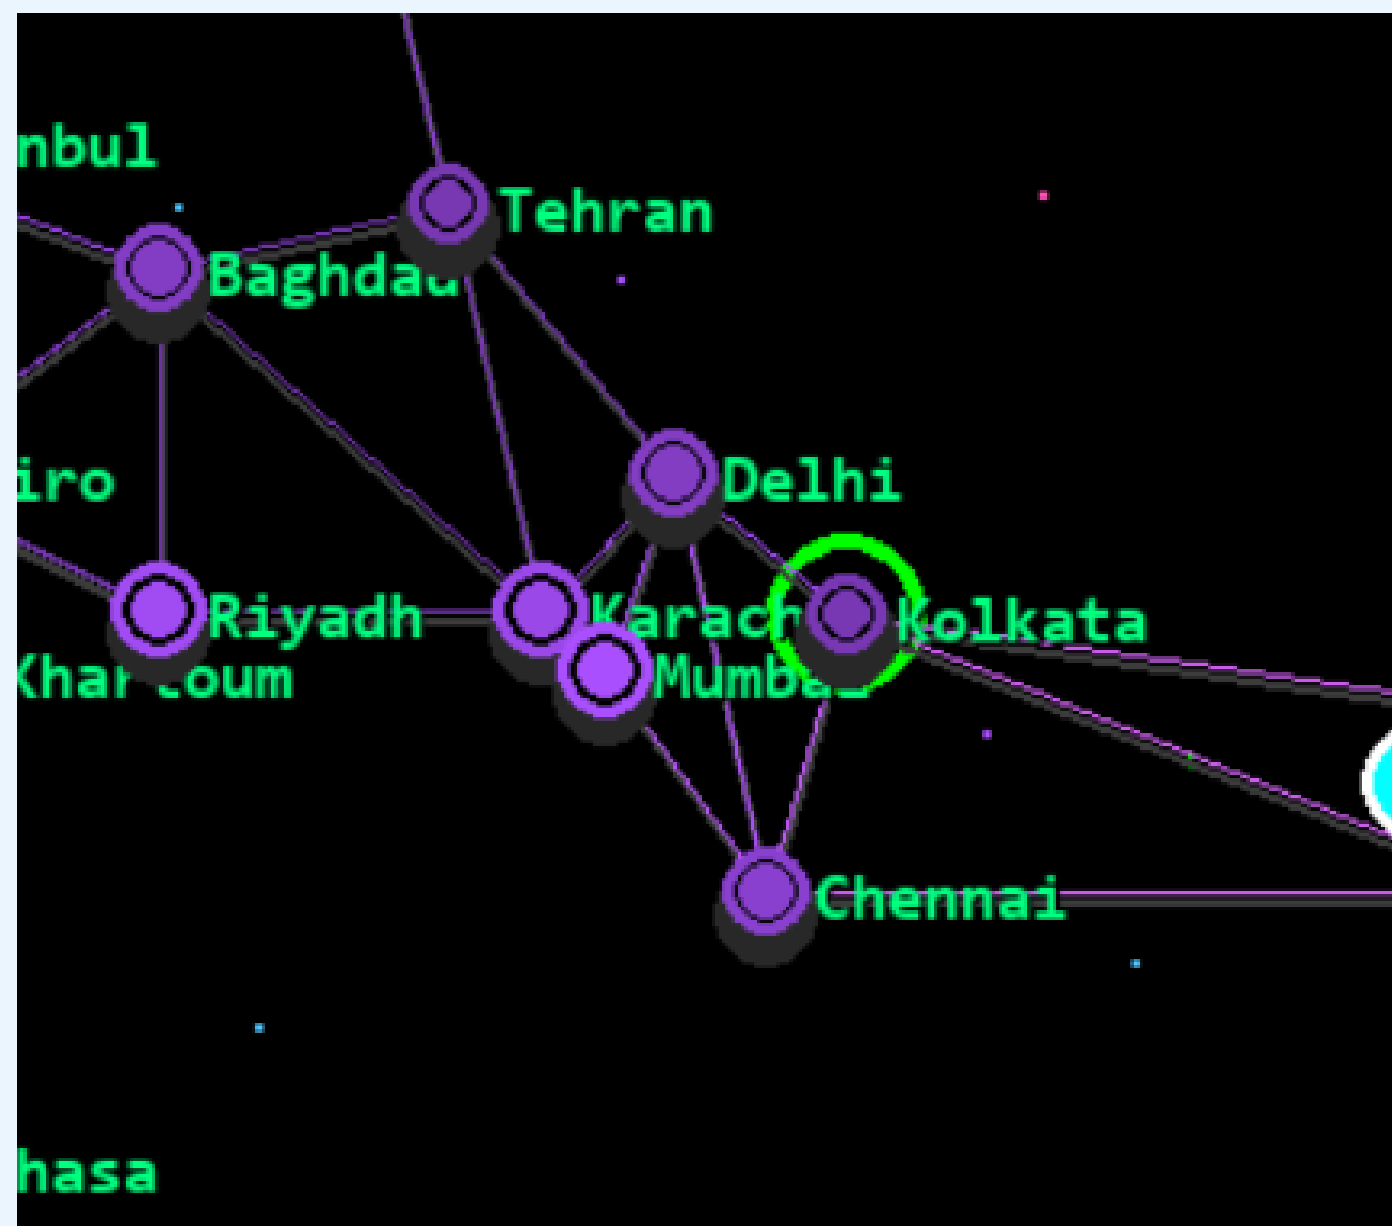

Demo - Construire Centro

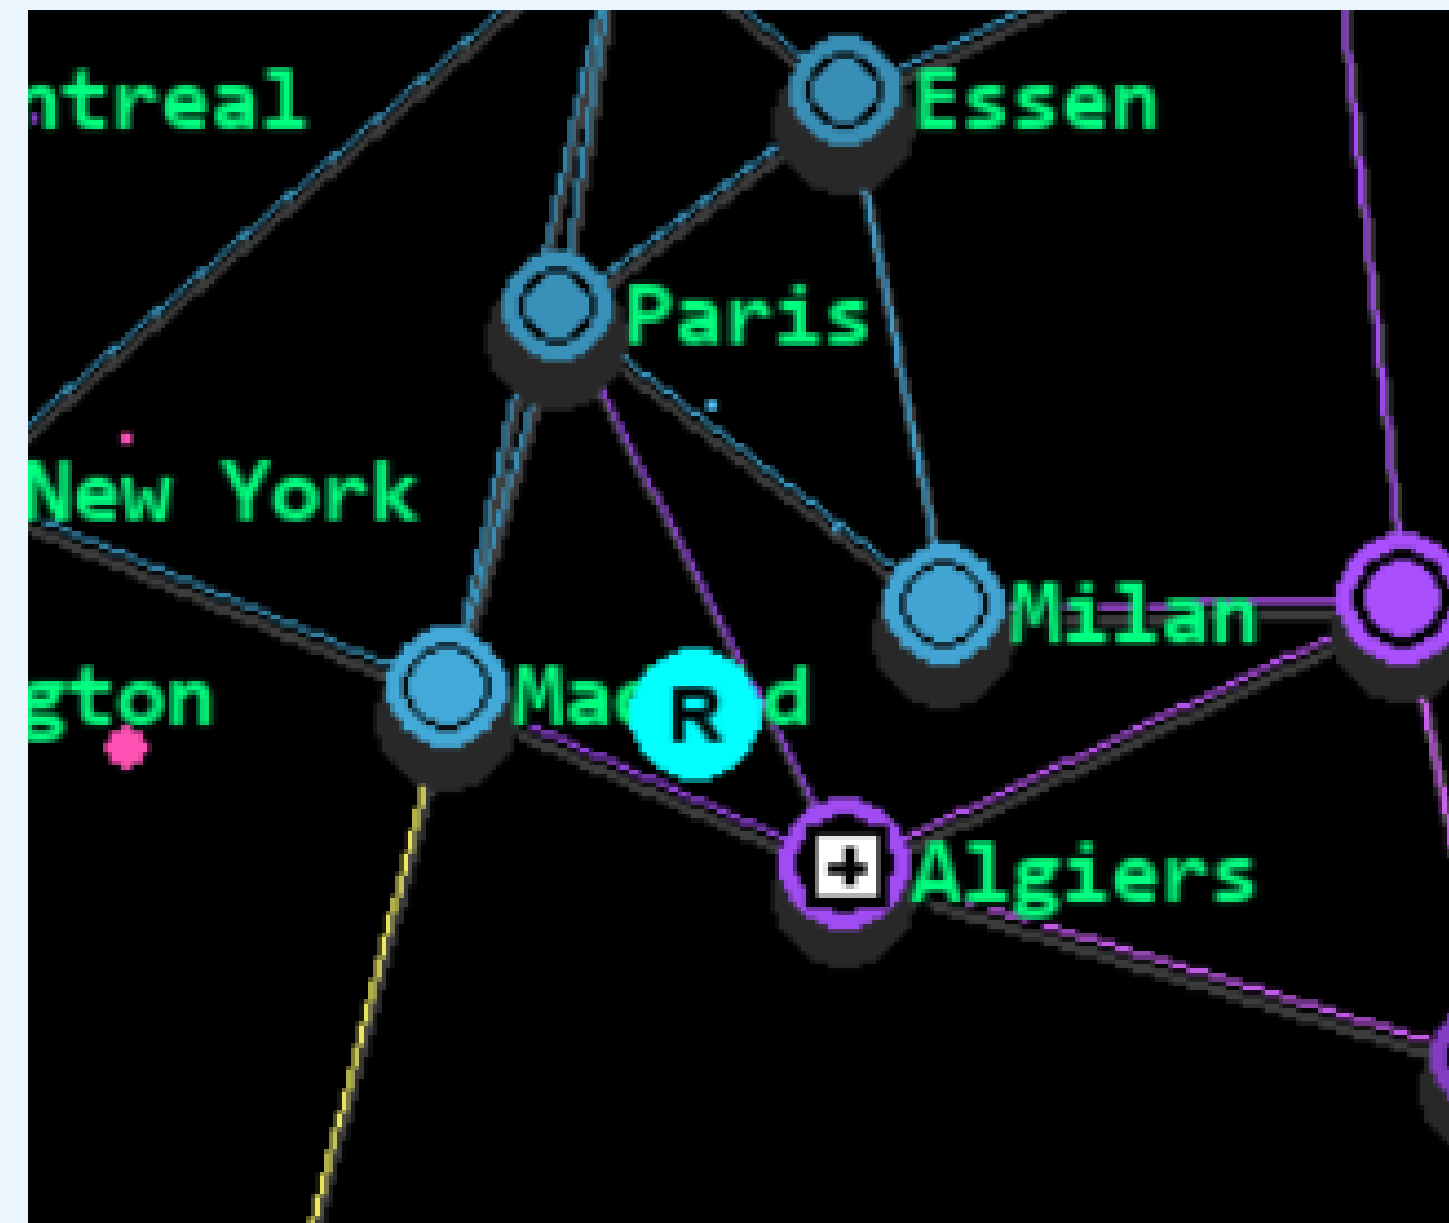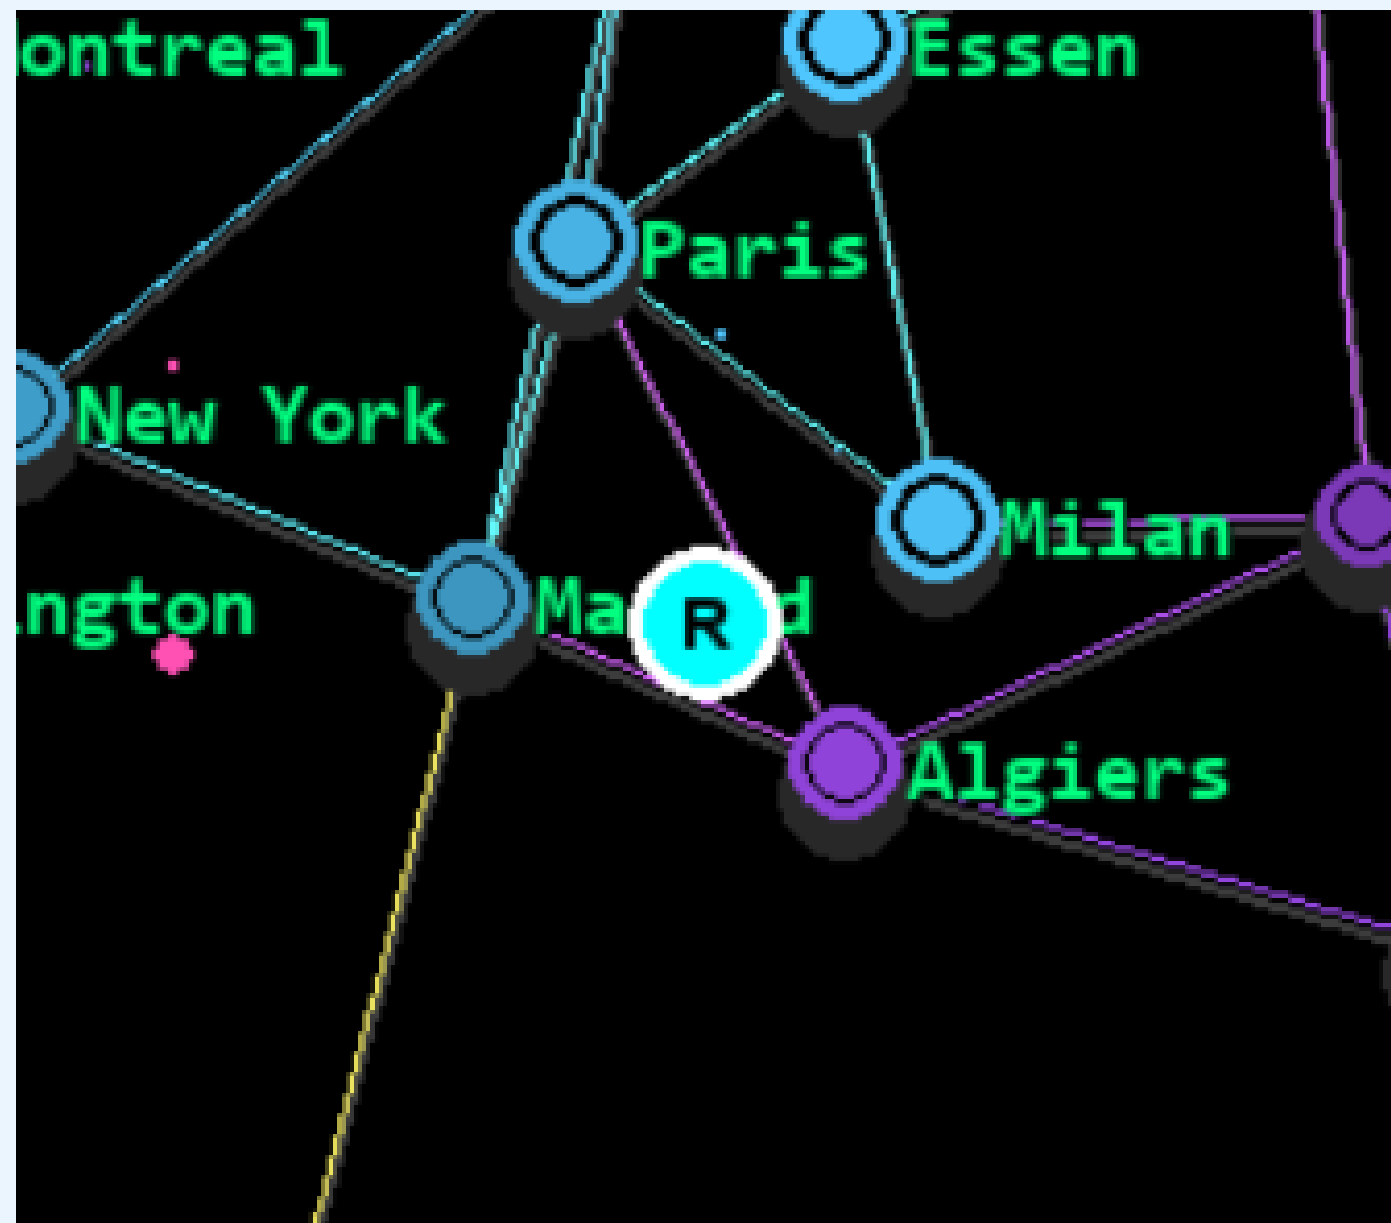

Demo - Encontrar Cura

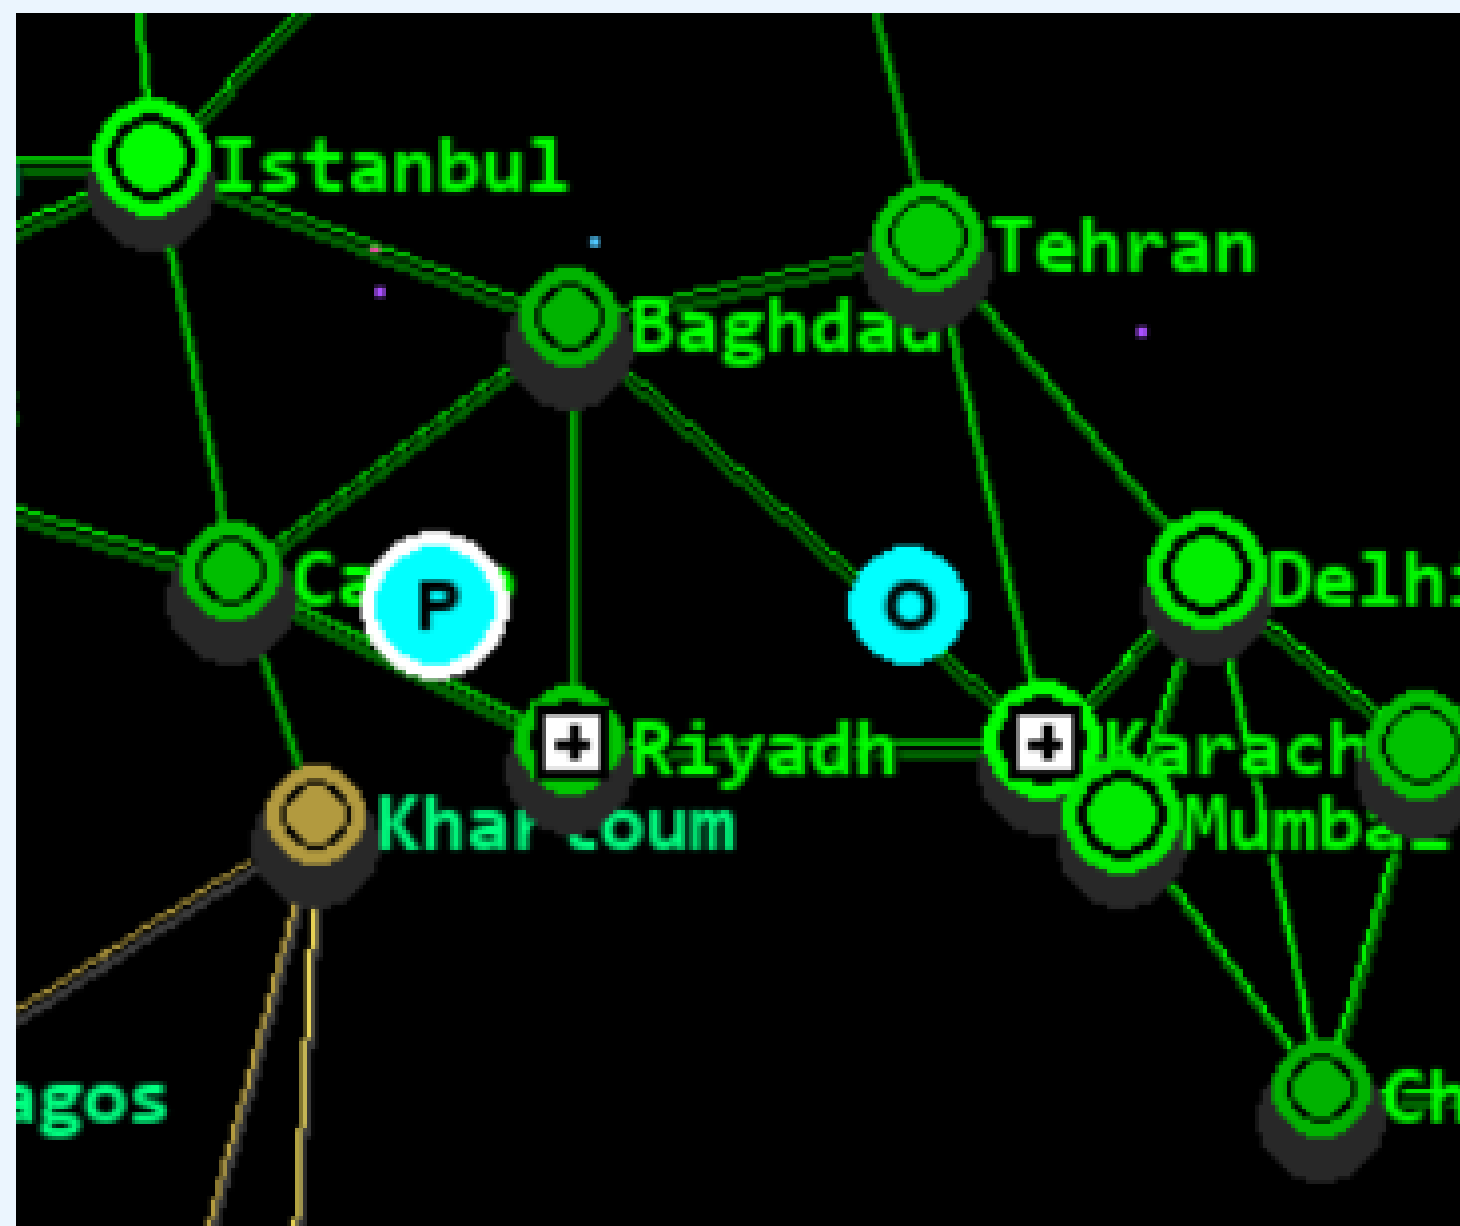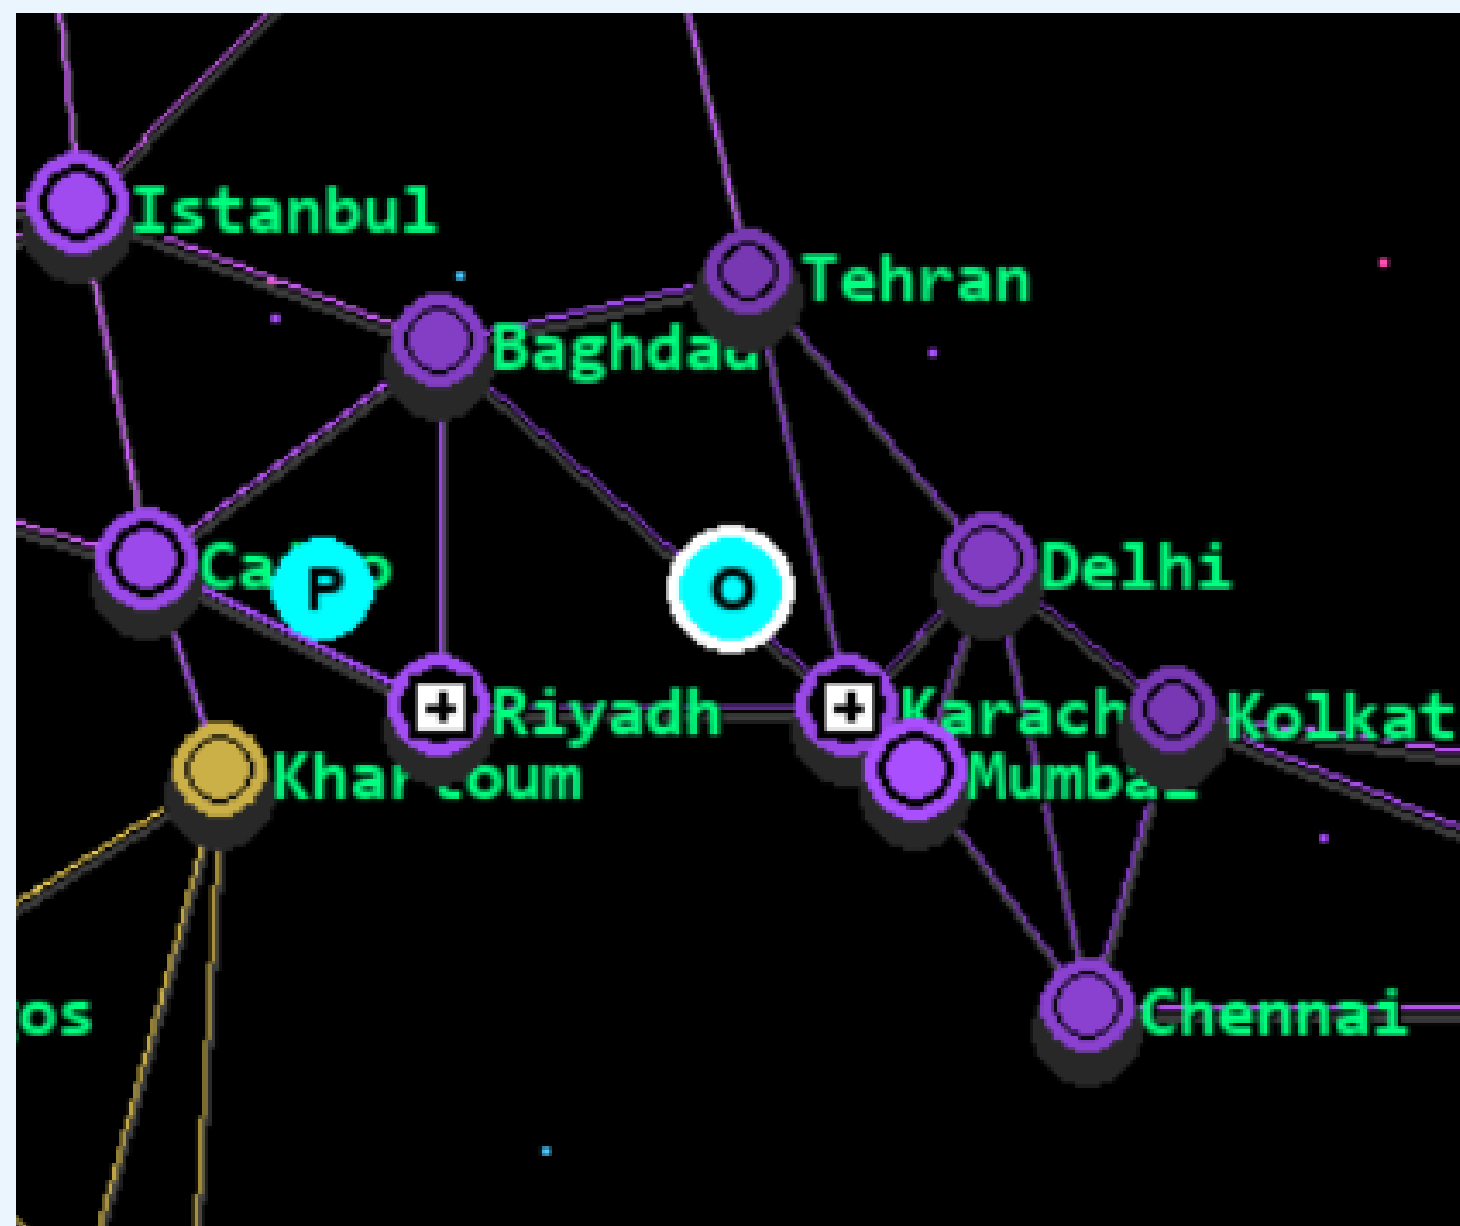

OBRIGADO!
